CITY of NOVI CITY COUNCIL



Agenda Item H March 26, 2018

SUBJECT: Approval of the final payment to Fonson Company, Inc., for the Meadowbrook Road and Pathway Settlement project in the amount of \$14,070.13, plus interest earned on retainage.

SUBMITTING DEPARTMENT: Department of Public Services, Engineering Division

CITY MANAGER APPROVAL:

EXPENDITURE REQUIRED	\$ 14,070.13
AMOUNT BUDGETED	\$ 634,847
APPROPRIATION REQUIRED	N/A
LINE ITEM NUMBER	202-202.00-865.173

BACKGROUND INFORMATION:

There was a portion of Meadowbrook Road between Twelve Mile and Thirteen Mile Roads (just south of Burroughs Avenue, along the MSU Tollgate Farms property) that had noticeable pavement deflection due to underlying soils (see attached location map). This project implemented the recommendations of the geotechnical report, which included the removal of the existing roadway and pathway asphalt pavement as well as reconstructing the entire sub-base section with new aggregate and heavy-duty synthetic geo-cell interlayer. The attached pictures show a before, during, and after progression of the project. The construction contract was awarded for this project at the August 14, 2017 City Council meeting to Fonson Company, Inc., in the amount of \$171,206.40.

Engineering staff worked with the engineering consultant for this project, AECOM, to review and verify the final contract payment amount of \$14,070.13 that is due the contractor (Final Pay Estimate No. 2, attached). The City Attorney reviewed the documentation and found it to be in an acceptable form (Beth Saarela, March 5, 2018). There was one (1) approved change order issued for this project resulting in a decrease of \$30,603.77 to the construction contract, or 17.9% under the awarded amount. The approved change order resulted in a final contract price of \$140,602.63.

RECOMMENDED ACTION: Approval of the final payment to Fonson Company, Inc., for the Meadowbrook Road and Pathway Settlement project in the amount of \$14,070.13, plus interest earned on retainage.



Mep Author: J. Mathles Date: 5/24/17

Amended By Date Department

ad is not intended to replace cysoarce. This map was into ds and use the n a people of the O

MAP INTERPRETATION NOTICE

I as survey measurements performed or as defined in Michigan Public Act 1 ease contact the City GIS Manager to may information related to the map.



Roadway Reconstruction







240

R



Meadowbrook Road/Path Settlement Project



Before Construction



During Construction



After Construction



JOHNSON ROSATI SCHULTZ JOPPICH PC

27555 Executive Drive Suite 250 ~ Farmington Hills, Michigan 48331 Phone: 248.489.4100 | Fax: 248.489.1726

Elizabeth Kudla Saarela esaarela@jrsjlaw.com

www.jrsjlaw.com

March 5, 2018

Aaron Staup, Construction Engineer CITY OF NOVI Department of Public Services Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

Re: Meadowbrook Road and Path Repair – Fonson Company, Inc. -- Closing Documents

Dear Mr. Staup:

We have received and reviewed closing documents for the Meadowbrook Road and Path Repair:

- 1. Application for Final Payment
- 2. Contractor's Sworn Statement
- 3. Consent of Surety
- 4. Waivers of Lien

Subject to approval of the Application for Final Payment by appropriate City staff, the closing documents appear to be in order. The Maintenance Bond previously submitted with the Contract is sufficient to cover the final project cost. The General Contractor has provided its Full Unconditional Waiver of Lien prior to final payment.

Please feel free to contact me with any questions or concerns in regard to this matter.

Very truly yours,

JOHNSON, ROSATI, SCHULTZ & JOPPICH, P.C.

Elizabeth Kudla Saarela

C: Cortney Hanson, Clerk Carl Johnson, Finance Director/Chief Financial Officer George Melistas, Engineering Senior Manager Thomas R. Schultz, Esquire



PURCHASE ORDER NO.

95267

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Balance Due This Payment = \$ 14,070.13

					A	PP	PLICAT	ON FO	DF	{ FINA	L	PAYMEN	T						
ROJE	CT: Meadowbrook Road & Path	Repair		NO/	I PROJECT	NO.	.:	17-2301						PAYMENT NO .:		FINAL			
WNER	City of Novi 45175 W. Ten Mile Road Novi, Michigan 48375			ENGINEER:			AECOM - Great Lakes 27777 Franklin Road, Suite 2000 Southfield, Michigan 48034 (248) 204-5900				CONTRACTOR:		Fonson Company, Inc. 7644 Whitmore Lake Road Brighton, Michigan 48116 (810) 231-5188						
ONTR	ACT AMOUNT			FINAL COMPLETION DATES										DATES OF ESTI	MATE				
RIGIN	GINAL: \$171,206.40			\$171,206.40 ORIGINAL: REVISED:			i	November 1, 2017					FROM:		October 13, 2017				
EVISE	ED: \$140,602.6	3		ACTUAL:				-	(October 16,	201	7		TO:			December 6, 2017		
	SECTION 1.			COST OF COMPLETED WORK TO DATE															
ltern No.	MEADOWBROOK ROAD & PATH SET GL# 202-202.00-865.173 Description of Item	TLEMENT Unit			RACT ITEMS		nal) Total Amt		CON	TRACT ITEMS	(Re	vised) Total Amt	Quantity	THIS PERIOD		Quantity		TOTAL TO DATE	%
	Constr. Inspection "Crew Day"	CD	Quantity 25.00	S	640.00		16.000.00	Quantity 25.00	1\$	640.00	¢	16.000.00	Quantity	Amount	%	14.00	\$	8,960.00	56%
	Mobilization (10%)	LS	1.00	\$	17,500.00	\$	17,500.00	1.00	\$		\$	17,500.00			-	1.00	\$	17.500.00	100%
_	Pre-Construction Audio/Visual	LS	1.00	s		\$	785.00	1.00	\$		\$	785.00			-	1.00	S	785.00	1009
-	Remove HMA Surface	SY	764.00	S		\$	6.035.60	832.02	\$		\$	6.572.96				832.02	\$	6,572.96	100%
4	Curb and Gutter, Remove	LF	400.00	\$	7.85	\$	3,140.00	175,00	s		\$	1.373.75			1	175.00	\$	1,373.75	100%
5	Sidewalk, Remove	SY	8.00	\$	37.00	\$	296.00	0.00	\$		S					0.00			
6	Roadway Grading	STA	2.00	\$	6,770.00	\$	13,540.00	1.75	\$	6,770.00	\$	11,847.50				1.75	\$	11,847.50	100%
7	Subgrade Undercutting, Type II	CY	100.00	\$	25.00	\$	2,500.00	0.00	\$	25.00	\$					0.00			
8	Silt Fence	LF	400.00	\$	3.75	\$	1.500.00	270.00	\$	3.75	\$	1,012.50				270.00	\$	1,012.50	100%
9	Curb and Gutter Inlet Filter	EA	2.00	S	110.00	\$	220.00	3.00	\$	110.00	\$	330.00				3.00	\$	330.00	100%
10	Tensar TX5 Geogrid	SY	658.00	\$	5.75	\$	3,783.50	462.80	\$	5.75	\$	2,661.10				462.80	\$	2,661.10	100%
11	Geosynthetic Paving Fabric	SY	538.00	\$	11.00	\$	5,918.00	453.33	\$	11.00	\$	4,986,63				453.33	\$	4,986.63	100%
12	6A Stone, 12-inch, for Stabilization	SY	538.00	\$	26.80	\$	14,418,40	0.00	\$	26.80	\$	· · · ·				0.00	_		
13	Agg Base, 21AA Limestone, 6-inch	SY	184.00	\$	18.80	\$	3,459.20	378.67	\$	18.80	\$	7,119.00				378.67	\$	7,119.00	1009
14	Agg Base, 21AA Limestone, 10"	SY	692.00	\$	17.10	\$	11.833.20	500.58	\$	17.10	\$	8,559.92				500.58	\$	8,559.92	100%
15	Dr Structure Cover, Type B	EA	1.00	\$		\$	580.00	0.00	\$		\$	•				0.00			
16	Dr Structure Cover, Adj, Case 1	EA	1.00	\$	1,250.00		1,250.00	1.00	\$	1,250.00	\$	1,250.00				1.00	\$	1,250.00	100%
	DPW Structure Cover, Adj, Case 1	EA	1.00	\$	1,250.00		1,250.00	0.00	\$		\$	•				0.00	1		
	Point Up Drainage Structure	EA	1.00	\$	195.00		195.00	0.00	\$		\$					0.00			
_	Reconstruct Drainage Structure	VF	1.00	\$	475.00	\$	475.00	0.00	\$		\$					0.00	_		
	Underdrain, Subgrade, O-G, 6-inch	LF	400.00	\$	19.60	\$	7,840.00	391.00	\$		\$	7,663.60				391.00		7,663.60	1009
	HMA, 5E10	TON	92.00	\$		\$	12,328.00	116.56	\$		\$	15,619.04				116.56	\$	15,619.04	100%
	HMA, 3E10	TON	137.00	\$	134.00	\$	18.358.00	0.00	\$		\$	•			-	0.00	-		_
	HMA Approach	TON	14.00	\$		\$	1,876.00	0.00	\$		\$	-				0.00	-		
24	Curb and Gutter, Conc, Det C4	LF	400.00	\$	24.00	\$	9,600.00	175.00	\$	24.00	\$	4,200.00				175.00	\$	4,200.00	1009



26300 Lee BeGole Dr. Novi, Michigan 48375 Tei: (248) 347-0454 Fax: (248) 735-5659

PROJECT:	Meadowbrook Road & Path Repair

APPLICATION FOR FINAL PAYMENT NOVI PROJECT NO .: 17-2301

PAYMENT NO .: FINAL

	SECTION 1.		_							COST	° OF	COMPLETED	WORK TO	DATE						
ltern	MEADOWBROOK SETTLEMENT, 0 GL# 202-202.00-865.173	Cont'd		CONT	RACT ITEMS	(Original)		C	CONT	RACT ITEMS	(Rev	vised)		THIS PEF	DOIR				TOTAL TO DATE	
No.	Description of Item	Unit	Quantity	(Cost/Unit	Total Amt		Quantity	0	Cost/Unit	_	Total Aml	Quantity	Amou	nt	%	Quantity		Amount	%
25	Sidewalk, Conc, 4-inch	SF	66.00	\$	5.00	\$ 330	0.00	0.00	\$	5.00							0.00			
26	Remove/Replace Décor. Fence	LF	200.00	\$	45.80	\$ 9,160	0.00	16.00	\$	45,80	\$	732.80					16.00	\$	732.80	100%
27	Barricade, Type III, H-I, Light, Furn	EA	13.00	\$	65.00	\$ 84	5.00	10.00	\$	65.00	\$	650.00					10.00	\$	650.00	100%
28	Barricade, Type III, H-I, Light, Oper	EA	13.00	\$	5.20	\$ 6	7.60	10.00	\$	5.20	\$	52.00					10.00	\$	52.00	100%
29	Channelizing Device, 42", Furn	EA	30.00	\$	11.44	\$ 34	3.20	30.00	\$	11.44	\$	343.20					30,00	\$	343.20	100%
30	Channelizing Device, 42". Oper	EA	30.00	\$	1.04	\$ 3	1.20	30.00	\$	1.04	\$	31.20					30.00	\$	31.20	100%
31	Lighted Arrow, Type C, Furn	EA	2.00	\$	520.00	\$ 1.040	0.00	0.00	\$	520.00							0.00			
32	Lighted Arrow, Type C, Oper	EA	2.00	\$	52.00	\$ 104	4.00	0.00	\$	52.00							0.00			
33	Minor Traffic Devices	LS	1.00	\$	4,350.00	\$ 4,350	0.00	1.00	\$	4.350.00	\$	4,350.00					1.00	\$	4,350.00	100%
34	Pavt Mrkg, Longit, 6" or less, Rem	LF	300.00	\$	0.95	\$ 28	5.00	300.00	\$	0.95	\$	285.00					300.00	\$	285.00	100%
35	Pavt Mrkg, W-R, Type R, 4". White	LF	180.00	\$	1.95	\$ 35	1.00	150.00	\$	1.95	\$	292.50					150.00	\$	292.50	100%
36	Pavt Mrkg, W-R, Type R, 4", Yellow	LF	180.00	\$	1.95	\$ 35	1.00	150.00	\$	1.95	\$	292.50					150.00	\$	292.50	100%
37	Plastic Drum, H-I, Furnish	EA	20.00	\$	13.52	\$ 27	0.40	26.00	\$	13.52	\$	351.52					26.00	\$	351.52	100%
38	Plastic Drum, H-I, Operate	EA	20.00	\$	1.04	\$ 20	0.80	26.00	\$	1.04	\$	27.04					26.00	\$	27.04	100%
39	Sign, Type B, Temp, Prism, Furn	SF	985.00	\$	3,12	\$ 3,07	3.20	513.00	\$	3.12	\$	1,600.56					513.00	\$	1,600.56	100%
40	Sign, Type B, Temp, Prism, Oper	SF	985.00	\$	0.26	\$ 25	6.10	513.00	\$	0.26	\$	133.38					513.00	\$	133.38	100%
41	Sign, Type B, Temp, Spec, Furn	SF	100.00	\$	3.38	\$ 33	8.00	90.00	\$	3.38	\$	304.20				1	90.00	\$	304.20	100%
42	Sign, Type B, Temp, Spec, Oper	SF	100.00	\$	0.26	\$ 2	6.00	90.00	S	0.26	s	23.40		· · · · · · · · · · · · · · · · · · ·			90.00	\$	23.40	100%
43	Traffic Regulator Control	LS	1.00	\$	500.00	\$ 50	0.00	1.00	\$	500.00	\$	500.00					1.00	\$	500.00	100%
44	Pedestrian Type II Barricade, Temp	EA	8.00	\$	78.00	\$ 62	4.00	8.00	\$	78.00	\$	624.00			_		8.00	\$	624.00	100%
45	Portable Mess Board, NTCIP, Furn	EA	2.00	\$	1,300.00	\$ 2.60	0.00	2.00	S	1,300.00	\$	2.600.00					2.00	\$	2,600.00	100%
46	Portable Mess Board, NTCIP, Oper	EA	2.00	\$	52.00	\$ 10-	4.00	2.00	\$	52.00	\$	104.00					2.00	\$	104.00	100%
47	Fence, Protective	LF	50.00	\$	6.00	\$ 30	0.00	0.00	\$	6.00	-						0.00			
48	Maintenance Gravel, LM	CY	100.00	\$	15.00	\$ 1.50	0.00	0.00	\$	15.00							0.00			
49	Pavt Mrkg, Thermo, 4", Yellow	LF	770.00	\$	1.50	\$ 1,15	5.00	695.00	\$	1.50	\$	1,042.50	_				695.00	\$	1,042.50	100%
50	Surface Restoration	LS	1.00	\$	4,500.00	\$ 4.50	0.00	1.00	\$	4,500.00	\$	4,500.00				-	1.00	\$	4.500.00	100%
_											_		_		_					
-																				
				-														-		
											-				_					
	TOTAL FROM THIS SHEET	•				\$ 32,52	5.50				\$	18,839.80		\$	-		15	\$	18,839.80	
	TOTAL FROM OTHER SHEET	-				\$ 138,68	0.90				\$	91,480.99		\$	-			\$	91,480.99	
	SUBTOTAL					\$ 171,20					\$	110.320.79		\$				\$	110,320.79	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

FINAL

APPLICATION FOR FINAL PAYMENT

PROJECT: Meadowbrook Road & Path Repair

NOVI PROJECT NO .:

17-2301

PAYMENT NO .:

NEW CONTRACT ITEMS

	SECTION 1.						COS	t of	COMPLETED	WORK TO	DATE						
ltern						NEW	CONTRAC	TITEN	MS		THIS PERIOD		TOTAL TO DATE				
No.	Description of Item	Unit	Division	GL#	Quantity	С	ost/Unit		Total Amt	Quantity	Amount	%	Quantity		Amount	%	
51	Pathway Grading	STA	0	GL# 202-202.00-865.173	2.50	\$	4.400.00	\$	11,000.00				2.50	\$	11,000.00	100%	
52	HMA, 3C	TON	0	GL# 202-202.00-865.173	149.82	\$	128.70	\$	19,281.83				149.82	\$	19,281.83	100%	
53			0	0	0.00	\$	4	\$	4				0.00	\$			
54			0	0	0.00	\$		s					0.00	\$	2		
55			0	0	0.00	\$	•	s				1	0.00	s			
56			0	0	0.00	\$		\$	9			1	0.00	\$	-		
57		_	0	0	0.00	\$	•	\$					0.00	s			
58			0	0	0.00	\$		\$					0.00	s			
59			0	0	0.00	\$		\$					0.00	\$	-		
60		-	0	0	0.00	\$	-	\$					0.00	\$			
61			0	0	0.00	\$		\$	×				0.00	\$			
62			0	0	0.00	\$	2	\$					0.00	\$			
63	· · · · · · · · · · · · · · · · · · ·		0	0	0.00	\$	÷.	\$					0.00	\$	2		
64			0	0	0.00	\$		\$				1	0.00	\$			
65			0	0	0.00	\$	12	\$			· · · · · ·		0.00	\$			
66			0	0	0.00	\$	<u>ب</u>	s	- ¥				0.00	5			
67			0	0	0.00	\$: • :	\$	-				0.00	\$			
68			0	0	0.00	\$	4	\$	4				0.00	\$			
69			0	0	0.00	\$	•	\$					0.00	\$	÷		
70			0	0	0.00	\$		\$					0.00	s	8		
71			0	0	0.00	\$	120	\$	4				0.00	\$			
72			0	0	0.00	\$		\$					0.00	\$	÷		
73			0	0	0.00	\$		\$					0.00	\$			
74			0	0	0.00	\$	14	\$					0.00	s			
75			0	0	0.00	\$	(e).	\$					0.00	\$	2		
76			0	0	0.00	\$		s	-				0.00	\$			
77			0	0	0.00	\$		\$					0.00	\$			
78			0	0	0.00	\$	200	s	•				0.00	\$	-		
1	TOTAL FROM THIS SHE	ET	1999 - Barris Barris (1999)					\$	30,281.83		\$ -			\$	30,281.83		
	TOTAL FROM OTHER SHEE	TS		\$ 171,206.40				\$	110,320,79		\$ -			\$	110,320.79		
	GRAND TOT	AL		\$ 171,206.40				\$	140,602.63		s -			\$	140,602.63	100%	




PURCHASE ORDER NO.

95267

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

riginal Contract Amount: \$ 171,206.40 CHANGE ORDERS hange Orders: \$ (30,603.77) No. Date djusted Contract Amount to Date: \$ 140,602.63 otal Cost of Work Performed to Date: \$ 140,602.63 total Cost of Contract and Extra Work to Date: \$ 140,602.63 total Cost of Contract and Extra Work to Date: \$ 140,602.63 total Cost of Laws over = \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	NT NO.: Amount (30,603.77)
ROJECT: Meadowbrook Road & Path Repair NOVI PROJECT NO.: 17-2301 PAYME riginal Contract Amount: \$ 171,206,40 CHANGE ORDERS hange Orders: \$ (30,603,77) No. Date djusted Contract Amount to Date: \$ 140,602.63 3 otal Cost of Work Performed to Date: \$ 140,602.63 3 INUS Retainage: 0% \$ - 6 INUS Inspection "Crew Days": To Date: \$ 140,602.63 9 INUS L.D.'s: # of days over = \$ - \$ \$ wubtotal: \$ 140,602.63 9 0 \$	<u>Amount</u> (30,603.77)
riginal Contract Amount: \$ 171,206.40 CHANGE ORDERS hange Orders: \$ (30,603.77) No. Date djusted Contract Amount to Date: \$ 140,602.63 3 otal Cost of Work Performed to Date: \$ 140,602.63 3 INUS Retainage: 0% 4 5 INUS Inspection "Crew Days": To Date 0% 4 5 INUS L.D.'s: # of days over = \$ 140,602.63 9 5 NUS L.D.'s: # of days over = \$ - 6 5 ubtotal: \$ 140,602.63 9 - 5 INUS L.D.'s: # of days over = \$ - \$ 5 yamount/day = \$600 \$ - \$ \$ \$ yamount/day = \$ - \$ \$ \$ \$ \$ Your State \$ 140,602.63 9 \$ \$ \$ Your State \$ - \$ \$ \$ \$ Your State \$ - </td <td><u>Amount</u> (30,603.77)</td>	<u>Amount</u> (30,603.77)
hange Orders:\$ $(30,603.77)$ No.Datedjusted Contract Amount to Date:\$140,602.631October 13,2017\$djusted Contract Amount to Date:\$140,602.63333otal Cost of Work Performed to Date:\$140,602.6345INUS Retainage:0%\$-65INUS Inspection "Crew Days":To Date $140,602.63$ 95INUS Inspection "Crew Days":To Date:\$140,602.639et Amt. Earned of Contract and Extra Work to Date:\$140,602.63910INUS L.D.'s:# of days over =\$-\$\$\$ amount/day =\$-\$\$\$ubtotal:\$140,602.63\$\$\$	(30,603.77)
djusted Contract Amount to Date:\$140,602.631October 13, 2017\$otal Cost of Work Performed to Date:\$140,602.6333	(30,603.77)
djusted Contract Amount to Date: total Cost of Work Performed to Date: NUS Retainage: INUS Retainage: INUS Inspection "Crew Days": To Date This Pay 0.00 \$ total Contract and Extra Work to Date: \$ 140,602.63 5 140,602.63 5 140,602.63 9 140,602.63 9 140,602.63 9 140,602.63 9 10 10 \$ \$ 140,602.63 9 10 10 \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	
batal Cost of Work Performed to Date: \$ 140,602.63 4 5 5 5	14
INUS Retainage: INUS Inspection "Crew Days": To Date This Pay 0.00 \$ - 6 14.00 \$ - 7 0.00 8 et Amt. Earned of Contract and Extra Work to Date: \$ 140,602.63 9 INUS L.D.'s: # of days over = \$ - \$ \$ amount/day = \$600 \$ 140,602.63 \$ ubtotal: \$ 140,602.63 \$	14) 12)
INUS Inspection "Crew Days": To Date This Pay 14.00 \$ 7 et Amt. Earned of Contract and Extra Work to Date: \$ 140,602.63 9 INUS L.D.'s: # of days over = \$ 10 \$ amount/day = \$ - \$ \$ 140,602.63 \$ \$ \$	14) 12)
This Pay 0.00 8 et Amt. Earned of Contract and Extra Work to Date: \$ 140,602.63 9 INUS L.D.'s: # of days over = \$ 10 \$ amount/day = \$ \$ \$ ubtotal: \$ 140,602.63 \$	-
et Amt. Earned of Contract and Extra Work to Date: \$ 140,602.63 9 10 10 10 \$ 10 \$ 10 \$ 10 \$ 10 \$ 10 \$ 1	14
INUS L.D.'s: # of days over = 10 \$ amount/day = \$ \$ \$ 140,602.63 \$	
\$ amount/day = \$600 \$ ubtotal: \$ 140,602.63 \$	14
ubtotal: \$ 140,602.63 \$	
	-
	•
DD Incentive "Crew Days", if under: \$ 7,040.00 TOTAL: \$	(30,603.77)
ubtotal: \$ 147,642.63	
INUS Amount of Previous Payments: \$ 133,572.50 1 \$ 133,572.50	
3 - Inspection "Crew Days" Allowed per Contra 4 \$ - Additional "Crew Days" per Change Orders	
5 \$ - Total inspection "Crew Days" Allowed:	25.00
6 \$ Inspection "Crew Days" Used to Date:	14.00
7 \$ Inspection "Crew Days" Remaining:	11.00
8 \$ - 9 \$ -	
10 \$ -	

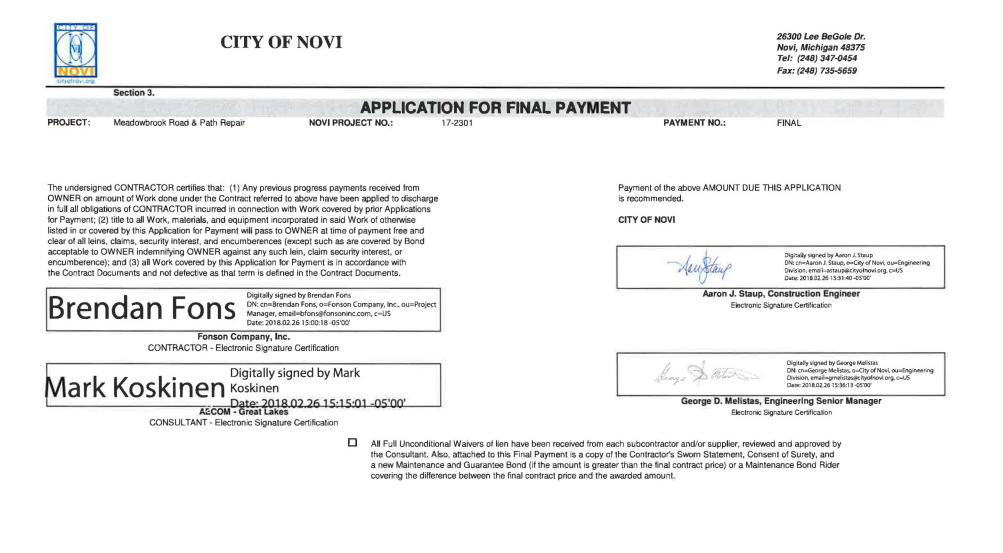

CONSENT OF SURETY **TO FINAL PAYMENT**

AIA DOCUMENT G707

PROJECT: Meadowbrook Road Reconstruction (name, address)

TO (Owner)

City of Novi 45175 Ten Mile Road Novi, MI 48375

ARCHITECT CONTRACTOR SURETY OTHER



ARCHITECT'S PROJECT NO: CONTRACT FOR: Road Reconstruction CONTRACT DATE:

Bond No. 8052114

CONTRACTOR: Fonson Company, Inc.

In accordance with the provisions of the Contract between the Owner and the Contractor as indicated above, the (here insert name and address of Surety Company)

Westfield Insurance Company One Park Circle, PO Box 5001 Westfield Center, OH 44251-5001 On bond of (here insert name and address of Contractor) Fonson Company, Inc. 7644 Whitmore Lake Rd. Brighton, MI 48116

,CONTRACTOR,

, OWNER,

SURETY COMPANY

hereby approves of the final payment to the Contractor, and agrees that final payment to the Contractor shall not relieve the (here insert name and address of Owner) Surety Company of any of its obligations to

11

City of Novi 45175 Ten Mile Road Novi, MI 48375

as set forth in the said Surety Company's bond.

IN WITNESS, the Surety Company has hereunto set its hand this

day of December, 2017

haluet ndel Attest.

(Seal):

ety Company				
Company	11	A A	1	
Tusa	Mr.	UV.	r.	
ature of Auth	orized Repu	resentative		

Title

AIA DOCUMENT G707 CONSENT OF SURETY COMPANY TO FINAL PAYMENT 1994 EDITION AIA 1994 AMERICAN INSTITUTE OF ARCHITECTS, 1735 NEW YORK AVENUE, NW, WASHINGTON, D.C. 20006-6292 G707-1994 General Power of Attorney

CERTIFIED COPY

POWER NO. 2140082 02 Westfield Insurance Co. Westfield National Insurance Co. Ohio Farmers Insurance Co.

Westfield Center, Ohio

Know All Men by These Presents, That WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY, corporations, hereinafter referred to individually as a "Company" and collectively as "Companies," duly organized and existing under the laws of the State of Ohio, and having its principal office in Westfield Center, Medina County, Ohio, do by these

presents make, constitute and appoint TERRI L. MAHAKIAN, MICHAEL M. HYLANT, JUDY K. WILSON, DEBORAH A. NEFF, CHALENE M. HADDON, LISA M. WILMOT, JOEL E. SPECKMAN, SUSAN E. HURD, VICKI S. DUNCAN, KRISTIE A. PUDVAN, MONICA M. MILLS, JOINTLY **OR SEVERALLY**

of ANN ARBOR and State of MI its true and lawful Attorney(s)-in-Fact, with full power and authority hereby conferred in its name. place and stead, to execute, acknowledge and deliver any and all bonds, recognizances, undertakings, or other instruments or contracts of suretyship-

LIMITATION: THIS POWER OF ATTORNEY GUARANTEE, OR BANK DEPOSITORY BONDS. THIS POWER OF ATTORNEY CANNOT BE USED TO EXECUTE NOTE GUARANTEE, MORTGAGE DEFICIENCY, MORTGAGE

GUARANTEE, OR BANK DEPOSITORY BONDS. and to bind any of the Company and duly attested by its Secretary, hereby ratifying and confirming all that the said Attorney(s)-in-Fact may do in the premises. Said appointment is made under and by authority of the following resolution adopted by the Board of Directors of each of the WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY: "Be It Resolved, that the President, any Senior Executive, any Secretary or any Fidelity & Surety Operations Executive or other Executive shall be and is hereby vested with full power and authority to appoint any one or more suitable persons as Attorney(s)-in-Fact to represent and act for and on behalf of the Company subject to the following provisions: "The Attorney-in-Fact. may be given full power and authority for and in the name of and on behalf of the Company, to execute, acknowledge and deliver, any and all bonds, recognizances, contracts, agreements of indemnity and other conditional or obligatory undertakings and any and all notices and documents canceling or terminating the Company's liability thereunder, and asteed and attested by the Corporate Secretary "Be it Further Resolved, that the signature of any such designated person and the seal of the Company heretofore or hereafter affixed to any power of attorney or any certificate relating thereto by facsimile, and any power of attorney or certificate bearing facsimile signatures or facsimile seal shall be valid and binding upon the Company with respect to any bond or undertaking to which it is attached." (Each adopted at a meeting held on February 8, 2000).



55.

SS.

WESTFIELD INSURANCE COMPANY WESTFIELD NATIONAL INSURANCE COMPANY OHIQ FARMERS INSURANCE COMPANY

S By

Dennis P. Baus, National Surety Leader and Senior Executive

On this 02nd day of JUNE A.D., 2017, before me personally came Dennis P. Baus to me known, who, being by me duly sworn, did depose and say, that he resides in Wooster, Ohio; that he is National Surety Leader and Senior Executive of WESTFIELD INSURANCE COMPANY, WESTFIELD INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY, the companies described in and which executed the above instrument; that he knows the seals of said Companies; that the seals affixed to said instrument are such corporate seals, that they were so affixed by order of the Boards of Directors of said Companies; and that he signed his name thereto by like order



County of Medina

State of Ohio County of Medina



David A. Kotnik, Attorney at Law. Notary Public My Commission Does Not Expire (Sec. 147.03 Ohio Revised Code)

I. Frank A. Carrino, Secretary of WESTFIELD INSURANCE COMPANY, WESTFIELD NATIONAL INSURANCE COMPANY and OHIO FARMERS INSURANCE COMPANY, do hereby certify that the above and foregoing is a true and correct copy of a Power of Attorney, executed by said Companies, which is still in full force and effect; and furthermore, the resolutions of the Boards of Directors, set out in the Power of Attorney are in full force and effect

In Witness Whereof, I have hereunto set my hand and affixed the seals of said Companies at Westfield Center, Ohio, this day of A.D.



BPOAC2 (combined) (06-02)



CONTRACTORS SWORN STATEMENT

The general contractor must execute this Sworn Statement. Prior to execution, the general contractor shall on Schedule B of this Sworn Statement list the names of all persons, firms, or corporations engaged by the General Contractor to furnish services, equipment, labor and/or materials in connection with the work performed on the premises including the type of work materials furnished by each.

The examining attorney shall verify that every person or firm listed in Schedule B has properly executed appropriate waivers of lien prior to issuance of any final payments.

STATE OF MICHIGAN

COUNTY OF Livingston

The undersigned, being duly sworn, on oath deposes and says that (s)he is the

Project Manager	of the	Fonson Company, Inc.	
(Title)		(Firm Name)	

the contractor employed by the City of Novi to furnish labor and materials for the

Meadowbrook Road Reconstruction

(Description of Improvement)

located at: City of Novi

The undersigned further states that all material (except as disclosed on said Schedule B) has been or will be furnished from his/her own stock and has been paid for in full; that there are no other contracts or subcontracts for said work outstanding, and that there is nothing due or to become due to any person for services, equipment, material, labor, or any other work done or to be done in connections with said work other than the stated on Schedule B. There are no chattel mortgages, personal property leases, conditional sale contracts or any other agreements given are now outstanding as to nay fixtures, equipment, appliances or materials placed upon or installed in or upon the aforementioned premises or improvements thereon. All waivers are true, correct, and genuine and are delivered unconditionally. Furthermore, there is no claim, either legal or equitable; to defeat the validity of said waivers.

Page 1 of 3

Signed this 15th day of February , 2018 Fonson Company, Fnc. (individual/corporation/partnership) Name: (Title) Project Magr Ву: Attest: 6 (Title) Subscribed and sworn to before me this _______ day of February, 2018 Notary Public: BARBARA A BARAN Notary Public - Michigan Livingston County My Commission Expires Mar 24, 2022 Acting In the County of Livingstrm

Page 2 of 3

Name of Subcontracting Firm	Type of Labor & Material Furnished	Amount of Contract	Amount Previously Paid to Date	Amount of Current Request	Accumalative Retainage to Date	Balance Due
Allied Construction	HMA Paving	\$45,269.50	\$45,269,50	\$0.00	0.0%	\$0.00
American Pavement Sawing, LLC	Sawcutting	\$621.50	\$621.50	\$0.00	0.0%	\$0.00
Core & Main LP	Material Supplier	\$1,010 58	\$1,010.58	\$0.00	0,0%	\$0.00
CSI Geoturf	Material Supplier	\$2,632.15	\$2,632.15	\$0.00	0.0%	\$0.00
Edw C Levy Co	Material Supplier	\$765.31	\$765.31	\$0.00	0.0%	\$0.00
Finishing Touch Photo & Video	Preconstruction Video	\$785.00	\$785.00	\$0.00	0.0%	\$0.00
GM & Sons, Inc.	Concrete Curb & Walks	\$4,200.00	\$4,200.00	\$0.00	0.0%	\$0.00
MacAllister CAT	Equipment Rental	\$700.66	\$700.66	\$0.00	0.0%	\$0.00
PK Contracting, Inc.	Pavement Markings	\$3,812.50	\$3,812.50	\$0,00	0.0%	\$0.00
Spartan Barricading & Traffic Control, Inc.	Traffic Control Barricades	\$7,168.98	\$7,168.98	\$0.00	0.0%	\$0.00
Stoneco of Michigan	Material Supplier	\$3,160.40	\$3,160.40	\$0.00	0.0%	\$0.00
					#DIV/0!	\$0.00
TOTALS		\$70,126.58	\$70,126.58	\$0.00		\$0.00

SCHEDULE B - CONTRACTORS SWORN STATEMENT

RECAPITULATION

Amount of Original Contract:	\$171,206.40	Work Completed to Date:	\$147,642 63
Plus: Extras to Contract:	-\$23,563.77	Less: Total Retainage:	\$0.00
Total: Contract plus Extras:	\$147,642.63	Less: Amount Previously Paid:	\$133,572.50
Less: Credits to Contract:	\$0.00	Less: Amount of this Request:	\$14,070.13
Total: Adjusted Contract:	\$147,642.63	Total Balance Due:	\$0.00



My/our contr		e Contracting Party)
	Labor & Materials (Type of service)	for the improvement of the property
described as		ok Road Reconstruction

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 2/15/18

24 C.

(Signature of Lien Claimant)

Brendan Fons (Printed Name of Lien Claimant)

Project Manager (Title of Lien Claimant)

Company	Name:	Fonson	Compai	ry, I	Enc,		-
Address:	7644	whitmor	e Lake	Rd.,	Brighton,	MI,4811	6
Telephone	: 810-	231-518	8				



My/our contract with	Fonson, Inc.	to provide	
10	(Prime C	ontracting Party)	
HMA Paving	ervice)	for the improvement of the property	
described as		rook Road Reconstruction	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if l/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

aus Murphy Shell Signed on: 1/18/18_

Dawn Microphy Shell (Printed Name of lien Chainfant) Accounts Receivalelo

Company Name: _____Allied Construction. Inc._____

Address: 9633 Northwest Court, Novi, MI 48347

Telephone: (248) 625-9581



My/our contract with	Fonson Company, Inc.	to provide
	(Prime Contracting Party)	
	for the improve	ement of the property
(Type of se	rvice)	
described as	Meadowbrook Road Reconstruction (Project Name)	<u> </u>

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 1-26 - 18

(Signature of Lien Claimant)

John Seguesc (Printed Name of Lien Claimant)

Cいいいして (Title of Lien Claimant)

Company	Name: Ar	which t	Aveninia	Sounds	,Luc	
		MANU				
		304-74				



My/our contract with	Fonson Company, Inc.	to provide
	(Prime Contracting Party)	
	for the improver	nent of the property
(Туре	of service)	
described as	Meadowbrook Road Reconstruction	
	(Project Name)	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 1-24-18 Kathy Quelcison (Signature of Lien Claimant)

(Printed Name of Lien Claimant)

Cridit Manafer

Company Na	ame:	Con	and W	thing	17KA	ND.	Supply	Waterwork	
Address:	Pb.F	Six 2	8330	St?	hours	mo	63146		

Telephone: 800_893.9150 × 201



My/our contract with	Fonson Company, Inc.	to provide
	(Prime Contracting Party)	•
	for the improv	ement of the property
(Туро с	ſservice)	
described as	Meadowbrook Road Reconstruction	n
	(Project Name)	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 1/23/18	Signature of Lien Claimant)
Ton	(Printed Name of Lien Claimant)
6	(Title of Lien Claimant)
Company Name: CSI GEOTUR	ŕ
Address: PO Box 668 Higher	OND HIL 48357
Telephone: 248-887-6767	27 U



j,

FULL UNCONDITIONAL WAIVER OF LIEN

My/our contrac	t with	Fonson Company, Inc.	to provide
		(Prime Contracting Party)	
	•		
		for the improv	ement of the property
	(Type of serv	ico)	
described as		Meadowbrook Road Reconstruction	m
		(Projeci Name)	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: A5/18 (Signature of Lien

AVEN L. TARTER (Printed Name of Lien Claimani)

ASST. CREDIT MON.

Company	Name: F	DWCL	evij			
Address:	9300	DIX-	DEARBOR	N, MI	48120	
Telephone	3/3.4	129.22	82			

•

....

FAX NO. :15867493340 810 231 5404

i.	ICITY_OF		
	FULL UNCONDITIONAL	, WAIVER OF L	
	My/our contract with FONSON C		_ to provide
	ALV SURVEY (Typo of service)	for the improvement of t	the property
	described as MEADOWGROOK		revenor?

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 111711	8((Signature of Lish Claimant)
U	-	O.HURLEY (Printed Name of Lien Claimant) OFRIER (Title of Lien Claimant)
Company Name:	FINISHING TOUCH PHOTO & VIDEO	
Address:	aroor of MILE RD.	148051
Telephone:	25095 23 MADE LD, M CHESTERFIELD, M (586) 749-3340	1 3002 -



My/our contract with	Fonson Company, Inc.	to provide
	(Prime Contracting Party)	
0	for the improv	vement of the property
(Туре с	(service)	
described as	Meadowbrook Road Reconstruction	011
	(Project Name)	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 01/23/18

(Signature of Lien (Jaimant)

Karl Schweitzer (Printed Name of Lien Claimant)

Manager

(Title of Lien Claimant)

Company Name: GM & Sons, Inc.

Address: 6784 Whitmore Lake Road, Whitmore Lake, MI 48189

Telephone: 734-929-1259

.

My/our contract with	Fonson Company, Inc.	to provide
	(Prime Contracting Party)	
	for the improver	nent of the property
(Гур	s of service)	
described as	Meadowbrook Road Reconstruction	
	(Project Name)	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 1-23-18

(Signature of Lien Claimant)

Prichard W. Slagencoke. (Printed Name of Lien Clamant)

Company Name:

Address:

Credit Mg Title of Lien Claimant) MacAllister / CAT 24800 Novi iEd xlovi M1 48375 (877) 659-4480

Telephone: (



My/our contract with		ny, Inc to provide
Pavement (Type	Markings of service)	for the improvement of the property
described as		Road Reconstruction

having been fully paid and satisfied, by signing this walver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 1232018	(Signature of Lien Claimpant)
	Nicole Gray, Agent
	(Printed Name of Lien Claimant)
	Agent
	(Title of Lion Claimant)
Company Name: P.K. Con-	tracting
Address: 19/15 Barrett Telephone: 248-362-213	Troy MI 48084
Telephone: 248-362-213	30



My/our contract with	Fonson Company, Inc.	to provide
1	(Prime Contracting Party)	
TRAFFIC Cept		ement of the property
described as	Meadowbrook Road Reconstruction	211
	(Project Name)	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: A 7 10

nney (Signature of Lien's

itle of Lien Claimant)

Cir ad lif Company Name: Address: Tir Telephone:



My/our contract with	Fonson Company, Inc.	to provide
	(Prime Contracting Party)	
	for the improv	provement of the property
(Type of so	rvice)	
described as	Meadowbrook Road Reconstruction	on
	(Project Name)	

having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.

If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.

Signed on: 123/18 of Lien Claimant) Claimant) Company Name: Store OF Michie S. Zeeb Road, Ann Arbor, MI 48103 Address: 210 Telephone: 7341-796-6755
