# CITY OF NOVI CITY COUNCIL FEBRUARY 22, 2021



**SUBJECT:** Consideration of approval of the final payments to Cadillac Asphalt, LLC for the 2018 and 2019 Neighborhood Road Program – Asphalt Streets in the amount of \$77,166.18 and \$48,686.36, respectively, plus interest earned on retainage.

**SUBMITTING DEPARTMENT:** Department of Public Works, Engineering Division

EXPENDITURE REQUIRED	\$ 8,125.00 expenditure
	\$ 69,041.18 retainage
	\$ 77,166.18 2018 NRP Asphalt
	\$ 9,081.16 expenditure
	\$ 39,605.20 retainage
	\$ 48,686.36 2019 NRP Asphalt
AMOUNT BUDGETED	\$ 8,125.00 2018 NRP Asphalt
	\$ 46,602.00 2019 NRP Asphalt
APPROPRIATION REQUIRED	\$ 0
LINE ITEM NUMBER	203-203.00-864.193 (2018 NRP Asphalt)
	203-203.00-864.203 (2019 NRP Asphalt)

**BACKGROUND INFORMATION:** The asphalt streets portion of the 2018 and 2019 Neighborhood Road Program (NRP) was advertised, bid, and awarded for a two-year contract to capture unit prices and lower the logistical costs of bidding and design separately. This process also allowed the City flexibility with regards to the scheduling of different project areas. The NRP work includes both asphalt rehabilitation and reconstruction of local roadways in an effort to preserve the longevity of the existing roadways in the City's network.

The following streets were selected and completed as part of the 2018 asphalt program: Heatherbrae Way, Siegal Drive, Siegal Court, Singh Boulevard, Vero Court, Churchill Boulevard, Island Lake Drive (portions), Anchorage Court and Crestwood Drive.

The following streets were selected and completed as part of the 2019 asphalt program: Lynnwood Drive, Warrington Drive, Warrington Court, Edinborough Drive, and Inverness Court.

This two-year construction contract was awarded at the May 21, 2018 City Council meeting to Cadillac Asphalt, LLC, in the amount of \$2,173,328.00. Staff worked with the engineering consultant for this project, AECOM-Great Lakes, to review and verify the final contract payment amounts of \$77,166.18 (2018) and \$48,686.36 (2019) that are due to the Contractor. The City Attorney reviewed the final documentation and found it to be in an acceptable form (Beth Saarela, February 2, 2021).

For the 2018 program, there were three (3) approved change orders issued resulting in a decrease of \$400.35 or 0.03% under the awarded amount. The approved change orders resulted in a final contract price of \$1,380,823.65 for the 2018 contract.

For the 2019 program, there was one (1) approved change order issued resulting in a decrease of \$116,645.42 or 14.7% under the awarded amount. The approved change orders resulted in a final contract price of \$675,458.58 for the 2019 contract.

**RECOMMENDED ACTION:** Approval of the final payments to Cadillac Asphalt, LLC for the 2018 and 2019 Neighborhood Road Program – Asphalt Streets in the amount of \$77,166.18 and \$48,686.36, respectively, plus interest earned on retainage.

### ELIZABETH KUDLA SAARELA

esaarela@rsjalaw.com

27555 Executive Drive, Suite 250 Farmington Hills, Michigan 48331 P 248.489.4100 | F 248.489.1726 www.rsjalaw.com



February 2, 2021

Aaron Staup, Construction Engineering Coordinator City of Novi Department of Public Works Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

Re: 2018 Neighborhood Roads Program - HMA

2019 Neighborhood Roads Program - HMA

**Cadillac Asphalt Closing Documents** 

Dear Mr. Staup:

We have received and reviewed closing documents for the 2018 and 2019 Neighborhood Roads Program Projects:

- 1. Applications for Final Payment (For Each Project)
- 2. Contractor's Sworn Statement (Cumulative)
- 3. Consent of Surety (Cumulative)
- 4. Waivers of Lien (Cumulative)

The closing documents appear to be in order. The Contractor will be required to provide its full unconditional waiver of lien *for each of the projects* in exchange for each final payment. The original Maintenance Bonds for each project are adequate given that the final project costs do not exceed the original project costs. Please feel free to contact me with any questions or concerns in regard to this matter.

Very truly yours,

ROSATI SCHULTZ JOPPICH

& AMTSBUECHLER PC

Elizabeth Kudla Saarela

**EKS** 


**Enclosures** 


C: Cortney Hanson, Clerk (w/Enclosures)

Carl Johnson, Finance Director/Chief Financial Officer (w/Enclosures)


Megan Mikus, Deputy Director of Public Works (w/Enclosures)

Thomas R. Schultz, Esquire (w/Enclosures)

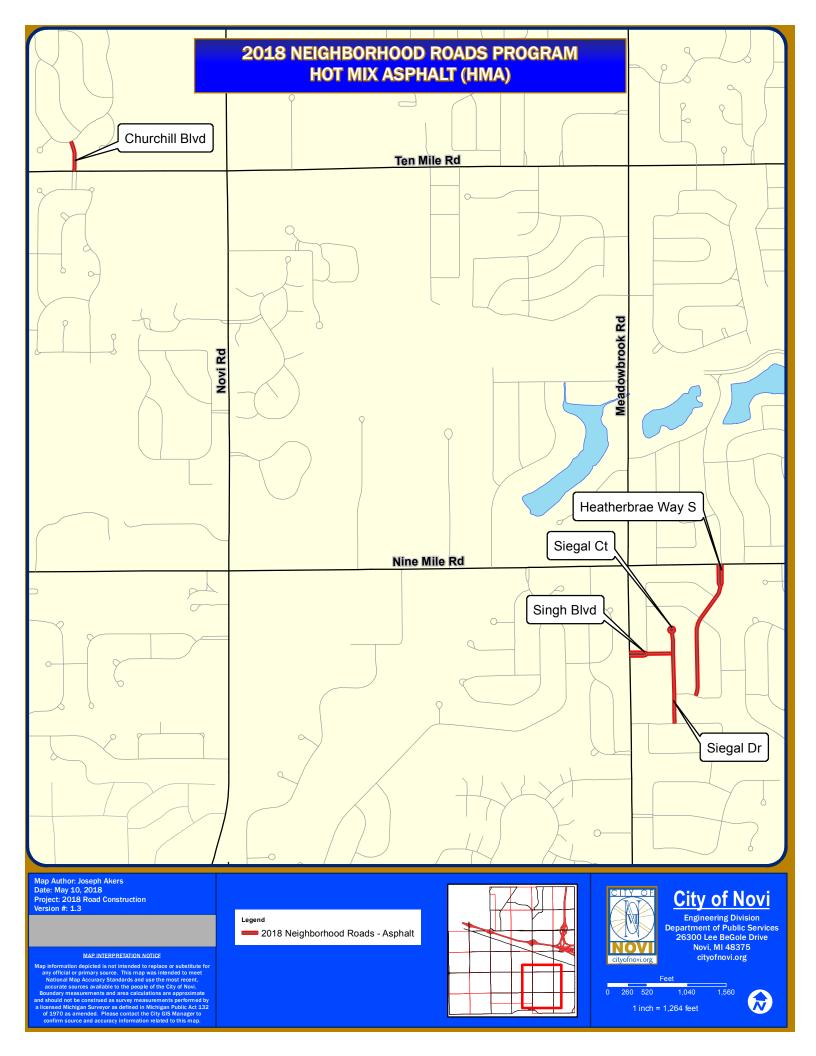

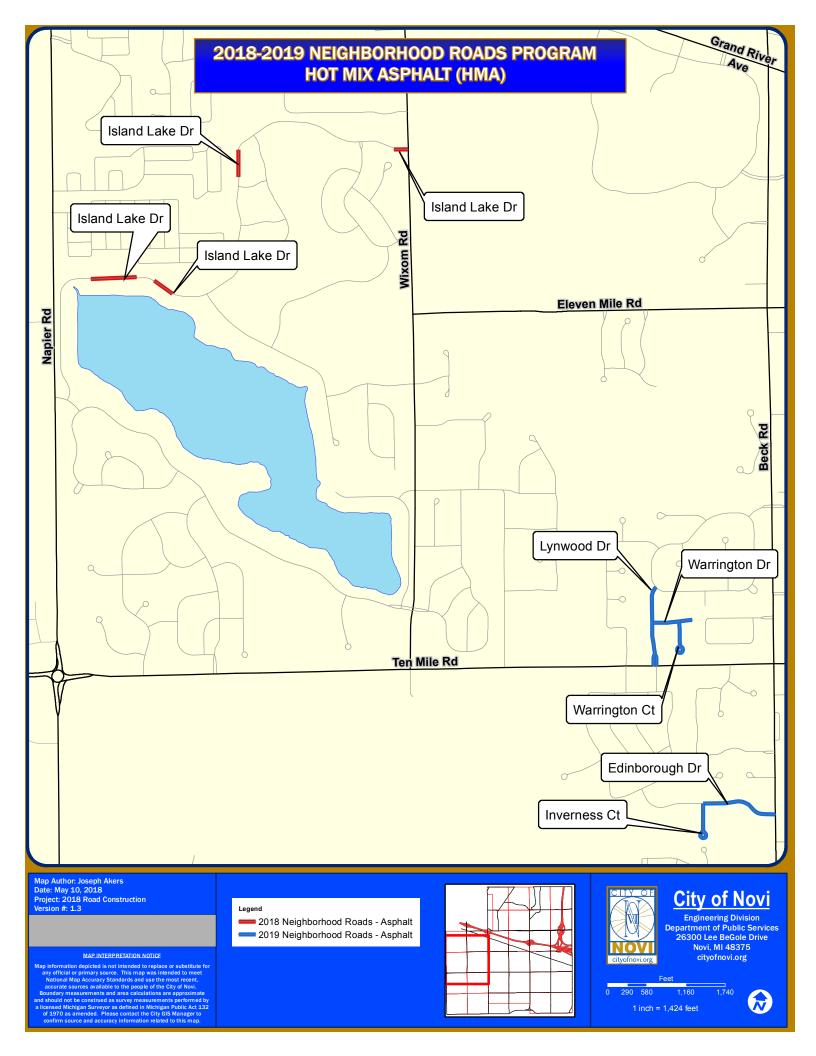

# 2018 NEIGHBORHOOD ROAD PROGRAM – ASPHALT STREETS

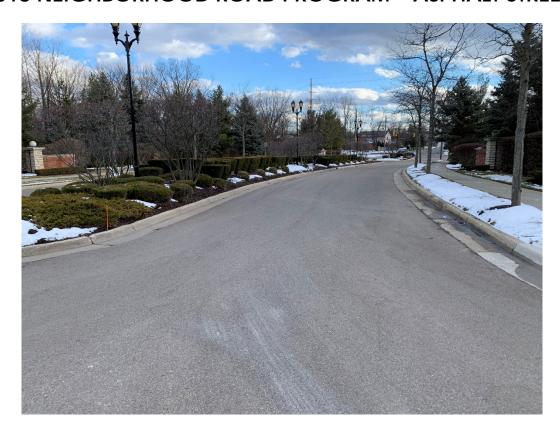

Churchill Boulevard (Churchill Crossing Sub) - Entranceway from 10 Mile



Churchill Boulevard (Churchill Crossing Sub) - Entranceway from Cavendish Ave



Siegal Drive (Turtle Creek Sub) - from Meridian Lane to Singh Boulevard




Siegal Court (Turtle Creek Sub) - Singh Boulevard to the cul-de-sac (First lift)



Singh Boulevard (Turtle Creek Sub) - at Siegal Drive/Court looking west



Singh Boulevard (Turtle Creek Sub) - at Cascade Drive looking south

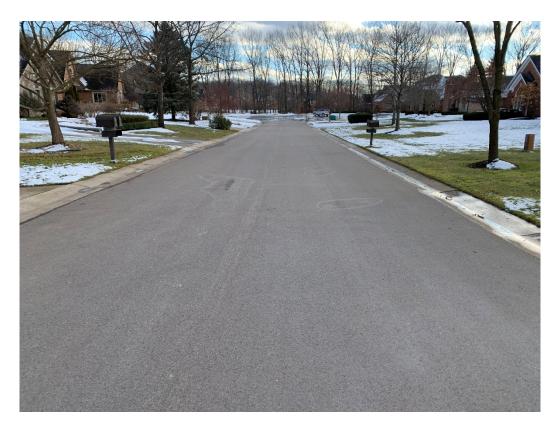


Vero Court (Vero Sub) - Looking west from Novi Road



Vero Court (Vero Sub) - Looking east from cul-de-sac

## 2019 NEIGHBORHOOD ROAD PROGRAM - ASPHALT STREETS

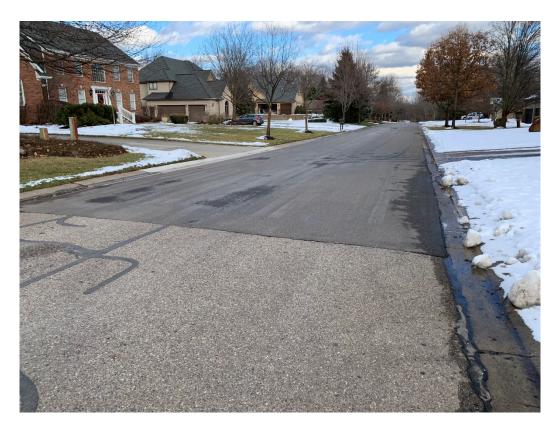

Edinborough Lane (Edinborough Sub) - Looking east towards Inverness Court



Lynwood Drive (Greenwood Oaks Sub) - Looking north from Warrington Drive



Lynwood Drive (Greenwood Oaks Sub) - Looking south towards 10 Mile

# NOVI citvofnovi, org

### **CITY OF NOVI**

Balance Due This Payment = \$ 77,166.18

PURCHASE ORDER NO. 95504 26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

**APPLICATION FOR FINAL PAYMENT** 

PROJECT: 2018 NRP - ASPHALT STREETS NOVI PROJECT NO.: 18-2102 PAYMENT NO.: FINAL

CIP NO.: 102-01

 OWNER:
 City of Novi
 ENGINEER:
 AECOM-Great Lakes
 CONTRACTOR:
 Cadillac Asphalt, LLC

 45175 W. Ten Mile Road
 27777 Franklin Road, Suite 2000
 51777 12 Mile Road

Novi, Michigan 48375 Southfield, Michigan 48034 (248) 204-5900

Wixom, Michigan 48393 (248) 380-3645

CONTRACT AMOUNT FINAL COMPLETION DATES DATES OF ESTIMATE

 ORIGINAL:
 \$1,381,224.00
 ORIGINAL:
 November 3, 2018
 FROM:
 July 11, 2019

 REVISED:

**REVISED:** \$1,380,823.65 **ACTUAL: TO:** June 25, 2020

### SECTION 1. COST OF COMPLETED WORK TO DATE

Item	2018 NRP - ASPHALT STREET GL# 203-203.00-864.193	r <u>s</u>	(	CONTRACT ITEM	IS (Oriç	ginal)	C	ON	ITRACT ITEMS	S (Re	vised)		THIS PERIOD		TOTAL TO DATE			
No.	Description of Item	Unit	Quantity	Cost/Unit		Total Amt	Quantity		Cost/Unit		Total Amt	Quantity	Amount	%	Quantity		Amount	%
0	Constr. Inspection "Crew Day"	CD	60.00	\$ 700.0	\$	42,000.00	60.00	\$	700.00	\$	42,000.00				129.00	\$	90,300.00	215%
1	Mobilization, Max 10%	LS	1.00	\$ 57,500.0	\$	57,500.00	1.00	\$	57,500.00	\$	57,500.00				1.00	\$	57,500.00	100%
2	Pre-Construction Audio-Visual	LS	1.00	\$ 4,175.0	\$	4,175.00	1.00	\$	4,175.00	\$	4,175.00				1.00	\$	4,175.00	100%
3	HMA Surface, Remove	SY	12962.00	\$ 4.0	\$	51,848.00	12416.65	\$	4.00	\$	49,666.60				12416.65	\$	49,666.60	100%
4	HMA Cold Milling	SY	3938.00	\$ 4.0	\$	15,752.00	9121.78	\$	4.00	\$	36,487.12				9121.78	\$	36,487.12	100%
5	HMA Base Repair	SY	815.00	\$ 22.0	\$	17,930.00	219.24	\$	22.00	\$	4,823.28				219.24	\$	4,823.28	100%
6	Roadway Grading	STA	37.10	\$ 3,200.0	\$	118,720.00	35.00	\$	3,200.00	\$	112,000.00				35.00	\$	112,000.00	100%
7	Undercut, Special, 1x3	CY	415.00	\$ 60.0	\$	24,900.00	283.76	\$	60.00	\$	17,025.60				283.76	\$	17,025.60	100%
8	Silt Fence	LF	1400.00	\$ 2.0	\$	2,800.00	0.00	\$	2.00	\$	-				0.00			
9	Curb and Gutter, Inlet Filter	EA	35.00	\$ 75.0	\$	2,625.00	27.00	\$	75.00	\$	2,025.00				27.00	\$	2,025.00	100%
10	Driveway Opening, Conc, Det M	LF	119.00	\$ 22.0	\$	2,618.00	119.00	\$	22.00	\$	2,618.00				119.00	\$	2,618.00	100%
11	Sidewalk, Remove	SY	206.00	\$ 8.0	\$	1,648.00	217.07	\$	8.00	\$	1,736.56				217.07	\$	1,736.56	100%
12	Sidewalk Ramp, Conc, 6-inch	SF	1846.00	\$ 8.0	\$	14,768.00	1953.63	\$	8.00	\$	15,629.04				1953.63	\$	15,629.04	100%
13	Detectable Warning Surface	LF	90.00	\$ 30.0	\$	2,700.00	60.00	\$	30.00	\$	1,800.00				60.00	\$	1,800.00	100%
14	Agg Base, 21AA Limestone, 8-inch	SY	17269.00	\$ 10.0	\$	172,690.00	14923.30	\$	10.00	\$	149,233.00				14923.30	\$	149,233.00	100%
15	Agg Base, 21AA Limestone, 6-inch	SY	571.00	\$ 11.0	\$	6,281.00	474.32	\$	11.00	\$	5,217.52				474.32	\$	5,217.52	100%
16	Dr Structure, Remove	EA	3.00	\$ 650.0	\$	1,950.00	1.00	\$	650.00	\$	650.00				1.00	\$	650.00	100%
17	Dr Structure, 24-inch Dia	EA	3.00	\$ 1,575.0	\$	4,725.00	0.00	\$	1,575.00	\$	-				0.00			
18	Dr Structure Cover, Type J	EA	2.00	\$ 1,100.0	\$	2,200.00	0.00	\$	1,100.00	\$	-				0.00			į.
19	Dr Structure Cover, Type K	EA	1.00	\$ 810.0	\$	810.00	4.00	\$	810.00	\$	3,240.00				4.00	\$	3,240.00	100%
20	Dr Structure Cover, Adj, Case 1	EA	24.00	\$ 295.0	\$	7,080.00	16.00	\$	295.00	\$	4,720.00				16.00	\$	4,720.00	100%
21	Point-Up Drainage Structure	EA	24.00	\$ 175.0	\$	4,200.00	19.00	\$	175.00	\$	3,325.00				19.00	\$	3,325.00	100%
22	Underdrain, Subgrade, O-G, 6-inch	LF	7343.00	\$ 9.0	\$	66,087.00	6615.55	\$	9.00	\$	59,539.95				6615.55	\$	59,539.95	100%
23	Reconstruct Drainage Structure	VF	20.00	\$ 250.0	\$	5,000.00	7.00	\$	250.00	\$	1,750.00			, and the second	7.00	\$	1,750.00	100%
24	Dr Structure Tap, 6-inch	EA	37.00	\$ 200.0	\$	7,400.00	18.00	\$	200.00	\$	3,600.00				18.00	\$	3,600.00	100%



TOTAL FROM OTHER SHEET

SUBTOTAL

### CITY OF NOVI

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

536,761.67

1,347,504.85 100%

\$

### APPLICATION FOR FINAL PAYMENT

PROJECT: 2018 NRP - ASPHALT STREETS NOVI PROJECT NO.: 18-2102 PAYMENT NO.: FINAL

CIP NO.: 102-01

\$

596,407.00

\$ 1,381,224.00

SECTION 1. COST OF COMPLETED WORK TO DATE 2018 NRP - ASPHALT STREETS, Cont'd CONTRACT ITEMS (Original) CONTRACT ITEMS (Revised) THIS PERIOD TOTAL TO DATE GL# 203-203.00-864.193 Description of Item Cost/Unit Total Amt Quantity Cost/Unit Total Amt Amount HMA, 5E1 TON 2045.00 97.00 198,365.00 2512.46 243,708.62 243,708.62 25 97.00 2512.46 100% 26 HMA, 3C TON 2500.00 80.00 200.000.00 2575.18 80.00 206.014.40 2575.18 206.014.40 100% 27 HMA Approach TON 160.00 125.00 20,000.00 0.00 125.00 0.00 28 Curb and Gutter, Remove LF 9067.00 4.00 36,268.00 9255.40 4.00 37,021.60 9255.40 37,021.60 100% 29 Curb and Gutter, Conc, Det F2 LF 1127.00 22.00 24,794.00 1157.35 22.00 25,461.70 \$ 25,461.70 1157.35 100% 30 Curb and Gutter, Conc, Det D2 LF 7940.00 22.00 174,680.00 8098.05 22.00 178,157.10 8098.05 178,157.10 100% Concrete Driveway SY 340.00 69.00 23,460.00 377.14 69.00 26,022.66 377.14 26,022.66 31 100% 32 Pavement, Remove SY 340.00 15.00 5,100.00 377.14 15.00 5,657.10 377.14 5,657.10 100% 33 Conduit, SCH40, 4-inch LF 500.00 20.00 10.000.00 70.00 20.00 1.400.00 70.00 1.400.00 100% SF 34 Sign, Type IIIB, R1-1 38.00 50.00 1,900.00 0.00 50.00 0.00 SF 35 Sign, Type IIIB, R1-2 9.00 50.00 450.00 0.00 50.00 0.00 Permanent Pavement Markings LS 1.00 2,875.00 2,875.00 1.00 2,875.00 2,875.00 \$ 2,875.00 1.00 100% Maintaining Traffic LS 1.00 51.925.00 51,925.00 1.00 \$ 51.925.00 51.925.00 1.00 51.925.00 100% Surface Restoration LS 32,500.00 32,500.00 \$ 32,500.00 32,500.00 0.25 8,125.00 32,500.00 1.00 1.00 1.00 100% 39 RCOC Permit Allowance DLR 2500.00 1.00 2.500.00 0.00 1.00 0.00 TOTAL FROM THIS SHEET \$ 784,817.00 \$ 810,743.18 \$ 8,125.00 \$ 810,743.18

\$

536,761.67

\$ 1,347,504.85

\$

8,125.00



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

**APPLICATION FOR FINAL PAYMENT** 

2018 NRP - ASPHALT STREETS NOVI PROJECT NO.: PAYMENT NO.: PROJECT: 18-2102 FINAL

> CIP NO.: 102-01

### **NEW CONTRACT ITEMS**

	SECTION 1.		COST OF COMPLETED WORK TO DATE													
Item					NEW CONTRACT ITEMS THIS PERIOD							TOTAL TO DATE				
No.	Description of Item	Unit	Division	GL#	Quantity	Co	st/Unit		Total Amt	Quantity	Amount	%	Quantity	,	Amount	%
40	Culvert, Class A, 12 inch	Ft	1	203-203.00-864.193	140.00	\$	73.00	\$	10,220.00				140.00	\$	10,220.00	100%
41	Geogrid	SY	1	203-203.00-864.193	232.30	\$	5.00	\$	1,161.50				232.30	\$	1,161.50	100%
42	Hand Patch	Ton	1	203-203.00-864.193	89.54	\$	245.00	\$	21,937.30				89.54	\$	21,937.30	100%
43			0	0	0.00	\$	-	\$	-				0.00	\$	-	
44			0	0	0.00	\$	-	\$	-				0.00	\$	-	
45			0	0	0.00	\$	-	\$	-				0.00	\$	-	
46			0	0	0.00	\$	-	\$	-				0.00	\$	-	
47			0	0	0.00	\$	-	\$	-				0.00	\$	-	
48			0	0	0.00	\$	-	\$	-				0.00	\$	-	
49			0	0	0.00	\$	-	\$	-				0.00	\$	-	
50			0	0	0.00	\$	-	\$	-				0.00	\$	-	
51			0	0	0.00	\$	-	\$	-				0.00	\$	-	
52			0	0	0.00	\$	-	\$	-				0.00	\$	-	
53			0	0	0.00	\$	-	\$	-				0.00	\$	-	
54			0	0	0.00	\$	-	\$	-				0.00	\$	-	
55			0	0	0.00	\$	-	\$	-				0.00	\$	-	
56			0	0	0.00	\$	-	\$	-				0.00	\$	-	
57			0	0	0.00	\$	-	\$	-				0.00	\$	-	
58			0	0	0.00	\$	-	\$	-				0.00	\$	-	
59			0	0	0.00	\$	-	\$	-				0.00	\$	-	
60			0	0	0.00	\$	-	\$	-				0.00	\$	-	
61			0	0	0.00	\$	-	\$	-				0.00	\$	-	
62			0	0	0.00	\$	-	\$	-				0.00	\$	-	
63			0	0	0.00	\$	-	\$	-				0.00	\$	-	
64			0	0	0.00	\$	-	\$	-				0.00	\$	-	
65			0	0	0.00	\$	-	\$	-				0.00	\$	-	
66			0	0	0.00	\$	-	\$	-				0.00	\$	-	
67			0	0	0.00	\$	-	\$	-				0.00	\$	-	

TOTAL FROM THIS SHEET

TOTAL FROM OTHER SHEETS

\$ 1,381,224.00

33,318.80 \$ \$ 1,347,504.85 \$ \$ 8,125.00 \$

33,318.80

1,347,504.85

**GRAND TOTAL** 

\$ 1,381,224.00

\$ 1,380,823.65

8,125.00

\$

1,380,823.65 100%



10 \$

**BALANCE DUE THIS PAYMENT:** 

### **CITY OF NOVI**

PURCHASE ORDER NO. 95504 26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Section 2. **APPLICATION FOR FINAL PAYMENT** PROJECT: 2018 NRP - ASPHALT STREETS NOVI PROJECT NO.: 18-2102 PAYMENT NO .: FINAL CIP NO .: 102-01 **Original Contract Amount:** \$ 1,381,224.00 **CHANGE ORDERS Change Orders:** \$ Date (400.35)<u>Amount</u> October 10, 2018 \$ 810.00 Adjusted Contract Amount to Date: \$ 1,380,823.65 January 11, 2018 \$ 11,840.00 3 May 22, 2019 \$ (13,050.35) Total Cost of Work Performed to Date: \$ 1.380.823.65 4 5 MINUS Retainage: 0% \$ 6 MINUS Inspection "Crew Days": 129.00 \$ 48,300.00 7 To Date 8 This Pay 0.00 Net Amt. Earned of Contract and Extra Work to Date: 1,332,523.65 9 10 MINUS L.D.'s: # of days over = \$ \$ amount/day = \$1,300 Subtotal: \$ 1,332,523.65 ADD Incentive "Crew Days", if under: \$ TOTAL: \$ (400.35)Subtotal: \$ 1,332,523.65 MINUS Amount of Previous Payments: \$ 1.255.357.47 1 \$ 26.376.84 2 \$ 198.497.38 3 \$ 292,420.14 Inspection "Crew Days" Allowed per Contract: 60.00 238,475.31 Additional "Crew Days" per Change Orders: 0.00 4 \$ 185,893.39 Total Inspection "Crew Days" Allowed: 60.00 5 \$ 208,163.44 Inspection "Crew Days" Used to Date: 6 \$ 129.00 7 \$ 105,530.97 Inspection "Crew Days" Remaining: -69.00 8 \$ 9 \$

77,166.18



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

	Section 3.			
		APPLI	<b>CATION FOR FI</b>	FINAL PAYMENT
PROJECT:	2018 NRP - ASPHALT STREETS	NOVI PROJECT NO.: CIP NO.:	18-2102 102-01	PAYMENT NO.: FINAL
OWNER on a n full all oblig for Payment; isted in or co clear of all lei acceptable to encumberence	ned CONTRACTOR certifies that: (1) Any purpose to the Contract refations of CONTRACTOR incurred in conne (2) title to all Work, materials, and equipme vered by this Application for Payment will pass, claims, security interest, and encumbers OWNER indemnifying OWNER against an e); and (3) all Work covered by this Applica Documents and not defective as that term is	lerred to above have been applied to action with Work covered by prior Applint incorporated in said Work of other ass to OWNER at time of payment fir ences (except such as are covered by y such lein, claim security interest, or ation for Payment is in accordance wi	discharge plications wise ee and y Bond r	Payment of the above AMOUNT DUE THIS APPLICATION is recommended.  CITY OF NOVI
	Cadillac Asphalt, CONTRACTOR - Electronic Sign	nature Certification		Aaron J. Staup, Construction Engineer Electronic Signature Certification
	AECOM-Great La CONSULTANT - Electronic Sign			

All Full Unconditional Waivers of lien have been received from each subcontractor and/or supplier, reviewed and approved by the Consultant. Also, attached to this Final Payment is a copy of the Contractor's Sworn Statement, Consent of Surety, and a new Maintenance and Guarantee Bond (if the amount is greater than the final contract price) or a Maintenance Bond Rider covering the difference between the final contract price and the awarded amount.

OWNER:

City of Novi

Novi, Michigan 48375

## **CITY OF NOVI**

**Balance Due This Payment =** 

**PURCHASE ORDER NO.** 95929

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Wixom, Michigan 48393

(248) 380-3645

**APPLICATION FOR FINAL PAYMENT** 

PROJECT: 2019 NRP - ASPHALT NOVI PROJECT NO.: 19-2102 PAYMENT NO.: FINAL

CIP NO.: 102-01

**ENGINEER:** AECOM-Great Lakes CONTRACTOR: Cadillac Asphalt, LLC 45175 W. Ten Mile Road 51777 12 Mile Road

27777 Franklin Road, Suite 2000 Southfield, Michigan 48034

(248) 204-5900

**FINAL COMPLETION DATES CONTRACT AMOUNT DATES OF ESTIMATE** 

ORIGINAL: **ORIGINAL:** \$792,104.00 November 2, 2019 FROM: October 18, 2019 **REVISED:** 

ACTUAL: **REVISED:** \$637,936.74 June 25, 2020 TO:

#### **SECTION 1. COST OF COMPLETED WORK TO DATE**

	SECTION 1.		COST OF COMPLETED WORK TO DATE																
Item	2019 NRP - Asphalt Streets GL# 203-203.00-864.203		С	CONT	RACT ITEMS	(Original)	(	CONT	TRACT ITEMS	(Revised)			TH	HIS PERIOD		TOTAL TO DATE			
No.	Description of Item	Unit	Quantity		Cost/Unit	Total Amt	Quantity		Cost/Unit	Total Amt	Qua	antity		Amount	%	Quantity	Amo	unt	%
0	Constr. Inspection "Crew Day"	CD	50.00	\$	700.00	\$ 35,000.00	50.00	\$	700.00	\$ 35,000	00 2	2.00	\$	1,400.00	4%	50.00	\$	35,000.00	100%
1	Mobilization, Max. 10%	LS	1.00	\$	48,000.00	\$ 48,000.00	1.00	\$	48,000.00	\$ 48,000	00					1.00	\$	48,000.00	100%
2	Pre-Construction Audio-Visual	LS	1.00	\$	1,275.00	\$ 1,275.00	1.00	\$	1,275.00	\$ 1,275	00					1.00	\$	1,275.00	100%
3	HMA Surface, Removal	SY	6829.00	\$	4.00	\$ 27,316.00	4737.00	\$	4.00	\$ 18,948	00					4737.00	\$	18,948.00	100%
4	HMA Cold Milling	SY	5858.00	\$	4.00	\$ 23,432.00	5935.00	\$	4.00	\$ 23,740	00 77	7.00	\$	308.00	1%	5935.00	\$	23,740.00	100%
5	HMA Base Repair	SY	1235.00	\$	22.00	\$ 27,170.00	330.00	\$	22.00	\$ 7,260	00					330.00	\$	7,260.00	100%
6	Roadway Grading	STA	22.00	\$	3,200.00	\$ 70,400.00	22.00	\$	3,200.00	\$ 70,400	00					22.00	\$	70,400.00	100%
7	Undercut, Special, 1x3	CY	400.00	\$	60.00	\$ 24,000.00	83.50	\$	60.00	\$ 5,010	00					83.50	\$	5,010.00	100%
8	Silt Fence	LF	700.00	\$	2.00	\$ 1,400.00	0.00	\$	2.00	\$						0.00			
9	Curb and Gutter Inlet Filter	EA	20.00	\$	75.00	\$ 1,500.00	19.00	\$	75.00	\$ 1,425	00					19.00	\$	1,425.00	100%
10	Sidewalk, Remove	SY	172.00	\$	8.00	\$ 1,376.00	573.13	\$	8.00	\$ 4,585	04 42	22.20	\$	3,377.60	74%	573.13	\$	4,585.04	100%
11	Sidewalk Ramp, Conc, 6-inch	SF	1581.00	\$	8.00	\$ 12,648.00	1832.77	\$	8.00	\$ 14,662	16 35	6.77	\$	2,854.16	19%	1832.77	\$	14,662.16	100%
12	Detectable Warning Surface	LF	60.00	\$	30.00	\$ 1,800.00	106.00	\$	30.00	\$ 3,180	00 46	6.00	\$	1,380.00	43%	106.00	\$	3,180.00	100%
13	Agg Base, 21AA, Limestone, 8-inch	SY	8462.00	\$	10.00	\$ 84,620.00	7382.10	\$	10.00	\$ 73,821	00					7382.10	\$	73,821.00	100%
14	Agg Base, 21AA, Limestone, 6-inch	SY	379.00	\$	11.00	\$ 4,169.00	232.97	\$	11.00	\$ 2,562	67 74	4.44	\$	818.84	32%	232.97	\$	2,562.67	100%
15	Dr Structure, Remove	EA	2.00	\$	650.00	\$ 1,300.00	0.00	\$	650.00	\$						0.00			I
16	Dr Structure, 24-inch Dia	EA	2.00	\$	1,575.00	\$ 3,150.00	0.00	\$	1,575.00	\$						0.00			I
17	Dr Structure Cover, Type J	EA	1.00	\$	1,100.00	\$ 1,100.00	0.00	\$	1,100.00	\$						0.00			L
18	Dr Structure Cover, Type K	EA	1.00	\$	810.00	\$ 810.00	0.00	\$	810.00	\$						0.00			
19	Dr Structure Cover, Adj, Case 1	EA	19.00	\$	295.00	\$ 5,605.00	8.00	\$	295.00	\$ 2,360	00					8.00	\$	2,360.00	100%
20	Point Up Drainage Structure	EA	19.00	\$	175.00	\$ 3,325.00	0.00	\$	175.00	\$						0.00			
21	Underdrain, Subgrade, O-G, 6-inch	LF	4461.00	\$	9.00	\$ 40,149.00	4565.00	\$	9.00	\$ 41,085	00 10	4.00	\$	936.00	2%	4565.00	\$	41,085.00	100%
22	Reconstruct Drainage Structure	VF	10.00	\$	250.00	\$ 2,500.00	0.00	\$	250.00	\$						0.00			
23	Dr Structure Tap, 6-inch	EA	22.00	\$	200.00	\$ 4,400.00	14.00	\$	200.00	\$ 2,800	00					14.00	\$	2,800.00	100%
24	HMA, 5E1	TON	1535.00	\$	97.00	\$ 148,895.00	1530.33	\$	97.00	\$ 148,442	01					1530.33	\$ 1	48,442.01	100%



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

**APPLICATION FOR FINAL PAYMENT** 

PROJECT: 2019 NRP - ASPHALT NOVI PROJECT NO.: 19-2102 PAYMENT NO.: FINAL

**CIP NO.:** 102-01

	SECTION 1.	COST OF COMPLETED WORK TO DATE																	
Item	2019 NRP - Asphalt Streets, Conti GL# 203-203.00-864.203	<u>nued</u>		CONTR	RACT ITEMS	(Original)	(	CONT	TRACT ITEMS			WORK TO		HIS PERIOD		TOTAL TO DATE			
No.	Description of Item	Unit	Quantity	C	Cost/Unit	Total Amt	Quantity		Cost/Unit	Tota	al Amt	Quantity		Amount	%	Quantity		Amount	%
25	HMA, 3C	TON	1486.00	\$	80.00	\$ 118,880.00	868.01	\$	80.00	\$	69,440.80	-371.62	\$	(29,729.60)	-43%	868.01	\$	69,440.80	100%
26	HMA Approach	TON	254.00	\$	125.00	\$ 31,750.00	56.64	\$	125.00	\$	7,080.00	56.64	\$	7,080.00	100%	56.64	\$	7,080.00	100%
27	Curb and Gutter, Remove	LF	1532.00	\$	4.00	\$ 6,128.00	1559.50	\$	4.00	\$	6,238.00	138.75	\$	555.00	9%	1559.50	\$	6,238.00	100%
28	Curb and Gutter, Conc, Det F2	LF	60.00	\$	22.00	\$ 1,320.00	98.65	\$	22.00	\$	2,170.30	98.65	\$	2,170.30	100%	98.65	\$	2,170.30	100%
29	Curb and Gutter, Conc, Det D2	LF	1472.00	\$	22.00	\$ 32,384.00	1682.70	\$	22.00	\$	37,019.40	261.95	\$	5,762.90	16%	1682.70	\$	37,019.40	100%
30	Concrete Driveway	SY	203.00	\$	69.00	\$ 14,007.00	74.94	\$	69.00	\$	5,170.86	40.84	\$	2,817.96	54%	74.94	\$	5,170.86	100%
31	Pavement, Remove	SY	203.00	\$	15.00	\$ 3,045.00	34.10	\$	15.00	\$	511.50					34.10	\$	511.50	100%
32	Sign, Type IIIB, R1-1	SF	6.00	\$	50.00	\$ 300.00	0.00	\$	50.00							0.00			
33	Sign, Type IIIB, R1-2	SF	14.00	\$	50.00	\$ 700.00	0.00	\$	50.00							0.00			
34	Permanent Pavement Markings	LS	1.00	\$	750.00	\$ 750.00	1.00	\$	750.00	\$	750.00	1.00	\$	750.00	100%	1.00	\$	750.00	100%
35	Maintaining Traffic	LS	1.00	\$	30,000.00	\$ 30,000.00	1.00	\$	30,000.00	\$	30,000.00					1.00	\$	30,000.00	100%
36	Surface Restoration	LS	1.00	\$	10,000.00	\$ 10,000.00	1.00	\$	10,000.00	\$	10,000.00	1.00	\$	10,000.00	100%	1.00	\$	10,000.00	100%
37	RCOC Permit Allowance	DLR	2500.00	\$	1.00	\$ 2,500.00	0.00	\$	1.00							0.00			
																	1		
	TOTAL FROM THIS SHEET					\$ 251,764.00		•		\$ 1	168,380.86		\$	(593.44)			\$	168,380.86	
	TOTAL FROM OTHER SHEET					\$ 540,340.00					169,555.88		\$	9,674.60			\$	469,555.88	
	SUBTOTAL					\$ 792,104.00					37,936.74		\$	9,081.16			\$	637,936.74	100%
	SOBTOTAL					Ψ 132,104.00				Ψ	101,000.14		Ψ	3,001.10			Ψ	007,300.74	10070



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454

Fax: (248) 735-5659

# **APPLICATION FOR FINAL PAYMENT**

NOVI PROJECT NO.: PROJECT: 2019 NRP - ASPHALT 19-2102 PAYMENT NO.: FINAL

> CIP NO.: 102-01

## **NEW CONTRACT ITEMS**

	SECTION 1.				CO	ST OF	COMPLETED	WORK TO	DATE					
Item					NEW CONTRACT ITEMS					THIS PERIOD			TOTAL TO DATE	
No.	Description of Item	Unit	Division	GL#	Quantity	Cost/Unit		Total Amt	Quantity	Amount	%	Quantity	Amount	%
38			0	0	0.00	\$ -	\$	-				0.00	\$ -	
39			0	0	0.00	\$ -	\$	-				0.00	\$ -	
40			0	0	0.00	\$ -	\$	-				0.00	\$ -	
41			0	0	0.00	\$ -	\$	-				0.00	\$ -	
42			0	0	0.00	\$ -	\$	-				0.00	\$ -	
43			0	0	0.00	\$ -	\$	-				0.00	\$ -	
44			0	0	0.00	\$ -	\$	-				0.00	\$ -	
45			0	0	0.00	\$ -	\$	-				0.00	\$ -	
46			0	0	0.00	\$ -	\$	-				0.00	\$ -	
47			0	0	0.00	\$ -	\$	-				0.00	\$ -	
48			0	0	0.00	\$ -	\$	-				0.00	\$ -	
49			0	0	0.00	\$ -	\$	-				0.00	\$ -	
50			0	0	0.00	\$ -	\$	-				0.00	\$ -	
51			0	0	0.00	\$ -	\$	-				0.00	\$ -	
52			0	0	0.00	\$ -	\$	-				0.00	\$ -	
53			0	0	0.00	\$ -	\$	-				0.00	\$ -	
54			0	0	0.00	\$ -	\$	-				0.00	\$ -	
55			0	0	0.00	\$ -	\$	-				0.00	\$ -	
56			0	0	0.00	\$ -	\$	-				0.00	\$ -	
57			0	0	0.00	\$ -	\$	-				0.00	\$ -	
58			0	0	0.00	\$ -	\$	-				0.00	\$ -	
59			0	0	0.00	\$ -	\$	-				0.00	\$ -	
60			0	0	0.00	\$ -	\$	-				0.00	\$ -	
61			0	0	0.00	\$ -	\$	-				0.00	\$ -	
62			0	0	0.00	\$ -	\$	-				0.00	\$ -	
63			0	0	0.00	\$ -		-				0.00	\$ -	
64			0	0	0.00	\$ -	\$	-				0.00	\$ -	
65			0	0	0.00	\$ -	\$	-				0.00	\$ -	
<b>I</b>	TOTAL FROM THIS SHEE	<del>.</del> Т					\$	-		\$ -			\$ -	•
	TOTAL FROM OTHER SHEET			\$ 792,104.00			\$	637,936.74		\$ 9,081.16			\$ 637,936.7	1
	GRAND TOTA			\$ 792,104.00			\$	637,936.74		\$ 9,081.16			\$ 637,936.7	



PURCHASE ORDER NO. 95929

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Section 2.

Section 2.		
	APPLICAT	ION FOR FINAL PAYMENT
PROJECT: 2019 NRP - ASPHALT	NOVI PROJECT NO.: CIP NO.:	19-2102 <b>PAYMENT NO.</b> : FINAL 102-01
Original Contract Amount:	\$ 792,104.00	CHANGE ORDERS
Change Orders:	\$ (154,167.26	) <u>No.</u> <u>Date</u> <u>Amount</u> 1 October 22, 2019 \$ (116,645.42)
Adjusted Contract Amount to Date:	\$ 637,936.74	· · ·
Total Cost of Work Performed to Date:	\$ 637,936.74	4 5
		6 7 8
Net Amt. Earned of Contract and Extra Work to Date:	\$ 637,936.74	
MINUS L.D.'s: # of days over = \$ 1,300	\$ -	
Subtotal:  ADD Incentive "Crew Days", if under:	\$ 637,936.74 \$ -	TOTAL: \$ (154,167.26)
Subtotal:	\$ 637,936.74	
MINUS Amount of Previous Payments:  1 \$ 111,107.11 2 \$ 65,945.61	\$ 589,250.38	
3 \$ 42,931.19 4 \$ 369,266.47 5 \$ -		Inspection "Crew Days" Allowed per Contract: 50.00 Additional "Crew Days" per Change Orders: 0.00 Total Inspection "Crew Days" Allowed: 50.00
6 \$ - 7 \$ - 8 \$ -		Inspection "Crew Days" Used to Date: 50.00 Inspection "Crew Days" Remaining: 0.00
9 \$ - 10 \$ -		-
BALANCE DUE THIS PAYMENT:	\$ 48,686.36	



AECOM-Great Lakes
CONSULTANT - Electronic Signature Certification

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

## Section 3. **APPLICATION FOR FINAL PAYMENT** NOVI PROJECT NO.: 19-2102 PAYMENT NO.: FINAL PROJECT: 2019 NRP - ASPHALT CIP NO.: 102-01 The undersigned CONTRACTOR certifies that: (1) Any previous progress payments received from Payment of the above AMOUNT DUE THIS APPLICATION OWNER on amount of Work done under the Contract referred to above have been applied to discharge is recommended. in full all obligations of CONTRACTOR incurred in connection with Work covered by prior Applications for Payment; (2) title to all Work, materials, and equipment incorporated in said Work of otherwise **CITY OF NOVI** listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all leins, claims, security interest, and encumberences (except such as are covered by Bond acceptable to OWNER indemnifying OWNER against any such lein, claim security interest, or encumberence); and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective as that term is defined in the Contract Documents. Aaron J. Staup, Construction Engineer Electronic Signature Certification Cadillac Asphalt, LLC **CONTRACTOR - Electronic Signature Certification**

All Full Unconditional Waivers of lien have been received from each subcontractor and/or supplier, reviewed and approved by the Consultant. Also, attached to this Final Payment is a copy of the Contractor's Sworn Statement, Consent of Surety, and a new Maintenance and Guarantee Bond (if the amount is greater than the final contract price) or a Maintenance Bond Rider covering the difference between the final contract price and the awarded amount.

CONSENT OF	OWNER	
SURETY COMPANY	ARCHITECT	П
TO FINAL PAYMENT		
	CONTRACTOR	
	SURETY	X
	OTHER	
PROJECT: 2018-2019 HMA Neighborhood Roads Pro (name, address)	gram, AECOM Project #605686	693
TO (Owner)		
Cadillac Asphalt, L.L.C. 2575 S. Haggerty Road, Suite 100	CONTRA CERTOR	
Canton, MI 48188	CONTRACT FOR:	\$2,173,328.00
CONTRACTOR: City of Novi, Michigan Engineering Division 26300 Lee Begole Drive Novi, MI 48375	CONTRACT DATE:	06/01/2018
In accordance with the provisions of the Contract be indicated above, the (here insert name and address of St	etween the Owner and the urety Co.)	Contractor as
Western Surety Company, One Towne Square, Suite 1075, Sc	outhfield, MI 48076-3732	
		URETY COMPANY,
on bond of (here insert name and address of Contractor)		own in the state of the state o
2575 S. Haggerty Road, Suite 100, Canton, MI 48188	estantia opiidių 2,2,0,	
2373 G. Haggerty Road, Suite 100, Canton, Mil 46166		
hereby approves of the final payment to the Contrac Contractor shall not relieve the Surety Company of a address of Owner)  City of Novi, Michigan, Engineering Division, 26300 Lee Bego	any of its obligations to (he	, CONTRACTOR because to the ere insert name and
as set forth in the said Surety Company's Bond.		, OWNER,
IN WITNESS WHEREOF, Western Surety Company		
the Surety Company has hereunto set its hand this _	21st day of Decemb	<u>2020</u>
	Western Surety Company	y
ATTEST: SEAL)	Surety Com	
	Loretta J. Ravert - Attorn	ov in Foot

Form F6277

# Western Surety Company

### POWER OF ATTORNEY APPOINTING INDIVIDUAL ATTORNEY-IN-FACT

Know All Men By These Presents, That WESTERN SURETY COMPANY, a South Dakota corporation, is a duly organized and existing corporation having its principal office in the City of Sioux Falls, and State of South Dakota, and that it does by virtue of the signature and seal herein affixed hereby make, constitute and appoint

# Charles G Richmond, David M Underwood, Michael S Richmond, Loretta J Ravert, Individually

of Jackson, MI, its true and lawful Attorney(s)-in-Fact with full power and authority hereby conferred to sign, seal and execute for and on its behalf bonds, undertakings and other obligatory instruments of similar nature

### - In Unlimited Amounts -

and to bind it thereby as fully and to the same extent as if such instruments were signed by a duly authorized officer of the corporation and all the acts of said Attorney, pursuant to the authority hereby given, are hereby ratified and confirmed.

This Power of Attorney is made and executed pursuant to and by authority of the By-Law printed on the reverse hereof, duly adopted, as indicated, by the shareholders of the corporation.

In Witness Whereof, WESTERN SURETY COMPANY has caused these presents to be signed by its Vice President and its corporate seal to be hereto affixed on this 25th day of June, 2015.

WESTERN SURETY COMPANY

Paul T. Bruflat, Vice President

State of South Dakota
County of Minnehaha

On this 25th day of June, 2015, before me personally came Paul T. Bruflat, to me known, who, being by me duly sworn, did depose and say: that he resides in the City of Sioux Falls, State of South Dakota; that he is the Vice President of WESTERN SURETY COMPANY described in and which executed the above instrument; that he knows the seal of said corporation; that the seal affixed to the said instrument is such corporate seal; that it was so affixed pursuant to authority given by the Board of Directors of said corporation and that he signed his name thereto pursuant to like authority, and acknowledges same to be the act and deed of said corporation.

My commission expires
February 12, 2021



S. Eich, Notary Public

### CERTIFICATE

I, L. Nelson, Assistant Secretary of WESTERN SURETY COMPANY do hereby certify that the Power of Attorney hereinabove set forth is still in force, and further certify that the By-Law of the corporation printed on the reverse hereof is still in force. In testimony whereof I have hereunto subscribed my name and affixed the seal of the said corporation this 21st day of December, 2020.



WESTERN SURETY COMPANY

J. Relson, Assistant Secretary

### **Authorizing By-Law**

## ADOPTED BY THE SHAREHOLDERS OF WESTERN SURETY COMPANY

This Power of Attorney is made and executed pursuant to and by authority of the following By-Law duly adopted by the shareholders of the Company.

Section 7. All bonds, policies, undertakings, Powers of Attorney, or other obligations of the corporation shall be executed in the corporate name of the Company by the President, Secretary, and Assistant Secretary, Treasurer, or any Vice President, or by such other officers as the Board of Directors may authorize. The President, any Vice President, Secretary, any Assistant Secretary, or the Treasurer may appoint Attorneys in Fact or agents who shall have authority to issue bonds, policies, or undertakings in the name of the Company. The corporate seal is not necessary for the validity of any bonds, policies, undertakings, Powers of Attorney or other obligations of the corporation. The signature of any such officer and the corporate seal may be printed by facsimile.



### **CONTRACTORS SWORN STATEMENT**

The general contractor must execute this Sworn Statement. Prior to execution, the general contractor shall on Schedule B of this Sworn Statement list the names of all persons, firms, or corporations engaged by the General Contractor to furnish services, equipment, labor and/or materials in connection with the work performed on the premises including the type of work materials furnished by each.

The examining attorney shall verify that every person or firm listed in Schedule B has properly executed appropriate waivers of lien prior to issuance of any final payments.

STATE OF MICHIGAN	
COUNTY OF Oakland	
The undersigned, being duly sworn, on oath deposes	and says that (s)he is the
Construction Manager of the	Cadillac Asphalt, LLC ,
(Title)	(Firm Name)
the contractor employed by the City of Novi to furnish	labor and materials for the
2018/2019 City of Novi Roa	ad Rehab Program
(Description	n of Improvement)
located at: Multiple Locartons/Roads	s within the City of Novi
	0.39 of which I have received payment of e persons, firms, and corporations engaged by the
undersigned to have furnished services, equipment, la	
of the improvements on the premises; that the dollar a	
corporation on account of labor, services, equipment,	
premises; that as of this date, all work to be performe	
or any suppliers or subcontractors of the undersigned	
the Schedule B of this Sworn Statement, has been ful to the plans and specifications.	ny accepted by the owner and completed according
to the biane and abcomeations.	

The undersigned further states that all material (except as disclosed on said Schedule B) has been or will be furnished from his/her own stock and has been paid for in full; that there are no other contracts or subcontracts for said work outstanding, and that there is nothing due or to become due to any person for services, equipment, material, labor, or any other work done or to be done in connections with said work other than the stated on Schedule B. There are no chattel mortgages, personal property leases, conditional sale contracts or any other agreements given are now outstanding as to nay fixtures, equipment, appliances or materials placed upon or installed in or upon the aforementioned premises or improvements thereon. All waivers are true, correct, and genuine and are delivered unconditionally. Furthermore, there is no claim, either legal or equitable; to defeat the validity of said waivers.

	Signed this	18th	day of		January	, 2021	
Name	Dale R	McInt	yre Digitally si	gned by Dale R .01.18 13:20:50	McIntyre -05'00'		_
		3,3,3,4,0,3,	Dale McIntyre	- Cadillac As	phalt, LLC		
	ř						
Ву	: Constru	uction Man	ager	Attest: _			_
		(Title)				(Title)	
Subs	scribed and swo	orn to befo	re me this _	18th	day of	January	_, 2021
N	otary Public: (	Muy	Jo My J	Ledda 6 Middle	for for		
				-Ch 19	17-1		

## **NOTARY SEAL**

AMY JO MIDDLETON
NOTARY PUBLIC, MICHIGAN
COUNTY OF OAKLAND
My Commission Expires 10/19/2024
Acting in the County of

## **SCHEDULE B - CONTRACTORS SWORN STATEMENT**

Name of Subcontracting Firm	Type of Labor & Material Furnished	Amount of Contract	Amount Previously Paid to Date	Amount of Current Request	Accumalative Retainage to Date	Balance Due
PK Contracting	Markings	\$1,375.00	\$1,375.00	\$0.00	0.0%	\$0.00
Doan Companies	Concrete	\$310,261.68	\$310,261.68	\$0.00	0.0%	\$0.00
Finishing Touch	Video	\$5,450.00	\$5,450.00	\$0.00	0.0%	\$0.00
Miller Bros	Milling	\$54,157.35	\$54,157.35	\$0.00	0.0%	\$0.00
State Barricade	sigange	\$2,950.00	\$2,950.00	\$0.00	0.0%	\$0.00
Site Solutions	Site Restoration	\$36,742.25	\$36,742.25	\$0.00	0.0%	\$0.00
Mark Anthony	Structure/ Drainage	\$576,852.48	\$576,852.48	\$0.00	0.0%	\$0.00
					#D <b>I</b> V/0!	\$0.00
					#D <b>I</b> V/0!	\$0.00
					#D <b>I</b> V/0!	\$0.00
TOTALS		\$987,788.76	\$987,788.76	\$0.00		\$0.00

### **RECAPITULATION**

Total: Adjusted Contract:	\$2,018,760.39	Total Balance Due:	\$125,852.54
Less: Credits to Contract: _	\$154,567.61	Less: Amount of this Request:	
Total: Contract plus Extras:	\$2,173,328.00	Less: Amount Previously Paid:	\$1,892,907.85
Plus: Extras to Contract: _		Less: Total Retainage:	\$0.00
Amount of Original Contract:	\$2,173,328.00	Work Completed to Date:	\$2,018,760.39



My/our contract with	(Prime Contracting Party) to provide
audio-Vide	for the improvement of the property
described as 20	018/2019 NOVI NEIGHBORHOOD STREETS (Project Name)
having been fully paid a lien rights against such p	and satisfied, by signing this waiver, all my/our construction property are hereby waived and released.
owner or lessee of the Notice of Furnishing fro the owner, lessee, or de us, the owner, lessee, or	provided to property that is a residential structure and if the property or the owner's or lessee's designee has received a m me/one or us or if I/we are not required to provide one, and signee has not received this waiver directly from me/one of designee may not rely upon it without contacting me/one of elephone, or personally to verify that it is authentic.  CHATLE HURLEY  (Printed Name of Lien Claimant)  OFFICER  (Title of Lien Claimant)
Company Name:	
Address:	FINISHING TOUCH PHOTO & VIDEO 25095 25 MILE RD.
Telephone:	CHESTERFIELD, MI 48051 (586) 749-3340



Miscellaneous Concrete Work for the improvement of the property (Type of service)
described as2018/2019 City of Novi Road Rehabilitation Program (Project Name)
having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.
If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.  Signed on:  12-16-2020    Signature of Lien Claimant   John Senkowski   Printed Name of Lien Claimant
Manager (Title of Lien Claimant)
Company Name: Doan Construction Co.
Address: 3670 Carpenter Rd, Ypsilanti, Mi. 48197
Telephone:734-971-4678



My/our contract with Cadillac Asphalt to provide
(Prime Contracting Party)
Concrete Road Construction for the improvement of the property (Type of service)
described as MA18-012 Novi HMA Program-Novi Road Rehab Program (Project Name)
having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.
If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.  Signed on:  (Signature of Lien Claimant)
Bill Hartsock
(Printed Name of Lien Claimant)
Vice President (Title of Lien Claimant)
Company Name: Mark Anthony Contracting, Inc.
Address: 4844 Old Plank Road, Milford, MI 48381
Telephone: 248-606-7727

# **Cadillac Asphalt LLC**

## Release and Waiver of Lien Rights For Final and Complete Payment

Project:	512567. 2018-2019 City of Novi Road Rehab Program
	,
Subcontractor:	Miller Brothers Construction Inc PO Box 30 Archbold, OH 43502
equipment, and ma any claim on any la	hereby acknowledges receipt of payment in full from Cadillac Asphalt LLC for all work, aterial furnished to the above job and therefore waives and releases all rights to make abor and material bond covering the job, and waives and releases all mechanic's liens, quitable lien rights which the undersigned may have on the job.
interest in the jobs	lease is for the benefit of, and may be relied upon by, all persons holding any property ite, the construction lender, any construction fund holder, the prime contractor, and the ies on any labor and material bond.
materials, any and employment of suc indemnify and hold	loes hereby represent and warrant that the undersigned has fully paid for all labor and all welfare, pension, vacation or other contributions required to be made on account of ch laborers or mechanics so provided by the undersigned and does hereby agree to deach of the foregoing, the project, work of improvement and real property free and and all claims or liens through the date indicated herein.
subcontractor and/	ete on the project at this time and there will be no further billing to the above named for Cadillac Asphalt LLC. We will send you a new Preliminary Lien Notice if we are additional work on this project.
<b>Date:</b> 01/22/2021	Firm Name: Miller Bros. Const., Inc.
	By: Sun D. mjily
	Title: Vice Pres.



My/our contract with	e ASPHALT	to provide
	(Prime Contracting Party)	
PAVEMENT MARICINGS (Type of service)	for the improvement	of the property
described as 2018-19 Hovi K	(Project Name)	3
having been fully paid and satisfied lien rights against such property are l		our construction
If the improvement is provided to powner or lessee of the property or Notice of Furnishing from me/one or the owner, lessee, or designee has nus, the owner, lessee, or designee mus, either in writing, by telephone, or	the owner's or lessee's designeed us or if I/we are not required to protective this waiver directly ay not rely upon it without contains.	has received a provide one, and from me/one of acting me/one of
Signed on: 12/3/2020	(Signature of Lien Claimant	)
	William M Wines, Agent	
	(Printed Name of Lien Claima	nt)
	(Title of Lien Claimant)	
Company Name: PK CONTRAC	TING	
Address: 1965 BARRETT	TROY, M. 49084	
Telephone: <u>148</u> 326.2130		



My/our contract with Call (Prime Contracting Party) to provide
Type of service)  Onto de for the improvement of the property
described as Novi Noigh bor Mod Stroots Program (Project Name) 2018 + 2019
having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.
If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.
Signed on: 11-16-26 Vanua Hadly (Signature of Lien Claimant)
Varyssa Hadley (Printed Name of Lien Claimant)
SICIOHA V 9 (Title of Lien Claimant)
Company Name: STATE BARRICADES, INC.  24806 INDUSTRIAL HWY.
Address: WARREN, MI 48089
Telephone: 58075708282



\_\_\_\_\_to provide

1	Type of service) Sprinker legalist the improvement of the property
	described as 18/19 City of Novi Road Rehalo Avoquan
	having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.
	If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.
	Signed on: 17470 Mulley Hold (Signature of Lien Claimant)
	Brad ley Holmes (Printed Name of Lien Claimant)
	President (Title of Lien Claimant)
	Company Name: Site Solutions Luc
	Address: 4337 E. Grand River Ste 154
	Telephone: 810.973,0595
