

CITY OF NOVI CITY COUNCIL AUGUST 30, 2021

SUBJECT: Consideration of approval of the final payment to Anglin Civil, LLC, for the Bosco Fields project in the amount of \$113,767.80, plus interest earned on retainage.

SUBMITTING DEPARTMENT: Department of Public Works, Engineering Division Parks, Recreation & Cultural Services

EXPENDITURE	\$ 3,162.51 Expense-Bosco Property Improvements-CIP Fund
REQUIRED	\$ 9,107.50 Expense-Bosco Property Improvements-Tree Fund
REGUIRED	S 0 Expense-Segment 53 Sidewalk-Municipal Street Fund
	\$ 12,270.01 Total Expense
	\$ 101,497.79 Total Retainage
	\$ 113,767.80 Total Expense & Retainage
AMOUNT	\$ 6,543 Bosco Property Improvements-CIP Fund (FY2020-21 Budget)
BUDGETED	\$ 9,108 Bosco Property Improvements-Tree Fund (FY2020-21 Budget) \$ 0 Segment 53 Sidewalk-MS Fund (FY2020-21 Budget)
	\$ 15,651 TOTAL
APPROPRIATION REQUIRED	\$ 0
REGUIRED	
LINE-ITEM	400-691.00-977.028 Bosco Property Improvements-CIP Fund
NUMBER	209-691.00-977.028 Bosco Property Improvements-Tree Fund
	204-204.00-974.451 Segment 53 Sidewalk-Municipal Street Fund

BACKGROUND INFORMATION:

At the City Council meeting held on May 21, 2018, a long-term use agreement was approved with the Novi Community School District for the property located on the west side of Beck Road and the south side of 11 Mile Road that was undeveloped and vacant. The agreement allowed the City to make improvements and maintain the land as public park land, open for use by the general public, and not for private operation. No indoor recreation is permitted, and no permanent structures are allowed or planned, except for any storage or maintenance structures agreed upon by the City and the School District.

Given the conditions above in the agreement, the City planned, designed and constructed a multi-purpose sports, athletic, and recreational fields with related amenities. It includes gravel parking areas and access roads off Beck Road and off 11 Mile Road. The final construction layout includes 13 soccer fields of four sizes: 4v4, 7v7, 9v9, and 11v11.

The City also utilized monies from the tree fund to plant several species of trees around the park for shade, screening, and boundary delineation. Also, the City added sidewalk to the much-needed gap along the west side of Beck Road, from 11 Mile Road to the south Bosco Park boundary (CIP# 125-053, Segment 53).


The construction contract was awarded for this project at the October 22, 2018 City Council meeting to Anglin Civil, LLC, in the amount of \$1,931,663.68.

Engineering staff worked with the engineering consultant for this project, Spalding DeDecker, to review and verify the final contract payment amount of \$113,767.80 that is due the contractor (Final Pay Estimate No. 10). The City Attorney reviewed the documentation and found it to be in an acceptable form (Beth Saarela, October 12, 2020).

There were five (5) approved change orders issued for this project resulting in a net increase of \$98,292.19 to the construction contract, or 5.0% over the awarded amount. The approved change orders resulted in a final contract price of \$2,029,955.87.

To insure appropriate athletic turf development, staff will program fertilizations and maintenance for the rest of this year, and play will begin on the fields in 2022.


RECOMMENDED ACTION: Approval of the final payment to Anglin Civil, LLC, for the Bosco Fields project in the amount of \$113,767.80, plus interest earned on retainage.

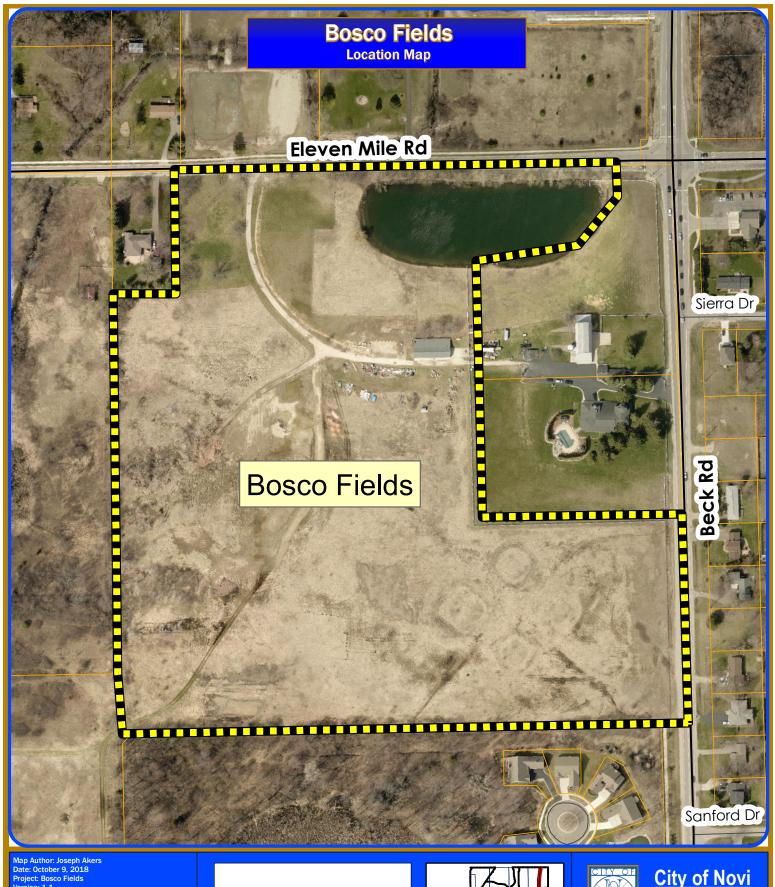




Amended By: Date:

MAP INTERPRETATION NOTICE





City of Novi

26300 Lee BeGole Drive Novi, MI 48375 cityofnovi.org





BOSCO FIELDS



Beck Road Entrance



Looking Northwest from Beck Road Entrance at 11v11 Fields



Looking west at southern access road and 11v11 Fields



Large gravel parking lot



11 Mile Road Entrance



Overall access drive, parking lot and fields from 11 Mile Road



7v7 and 4v4 fields from 11 Mile Road

ELIZABETH KUDLA SAARELA

esaarela@rsjalaw.com

27555 Executive Drive, Suite 250 Farmington Hills, Michigan 48331 P 248.489.4100 | F 248.489.1726 www.rsjalaw.com



October 12, 2020

Aaron Staup, Construction Engineering Coordinator City of Novi Department of Public Works Field Services Complex 26300 Lee BeGole Drive Novi, MI 48375

Re: Bosco Fields – Anglin Civil, LLC

Closing Documents

Dear Mr. Staup:

We have received and reviewed closing documents for the Bosco Fields Project:

- 1. Application for Final Payment
- 2. Contractor's Sworn Statement
- 3. Consent of Surety
- 4. Waivers of Lien
- Maintenance Bond Rider

The closing documents appear to be in order. The Contractor will be required to provide its full unconditional waiver of lien in exchange for the final payment. Please feel free to contact me with any questions or concerns in regard to this matter.

Very truly yours,

ROSATI SCHULTZ JOPPICH & AMPSBUECHLER PC

Elizabeth Kudla Saarela

EKS

C: Cortney Hanson, Clerk
Carl Johnson, Finance Director/Chief Financial Officer
Megan Mikus, Deputy Director of Public Works
Thomas R. Schultz, Esquire

OWNER:

CONTRACT AMOUNT

City of Novi

45175 W. Ten Mile Road

Novi, Michigan 48375

CITY OF NOVI

Balance Due This Payment = \$ 113,767.80 **PURCHASE ORDER NO.** 95681

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Anglin Civil, LLC

(248) 397-4200

13000 Newburgh Road

Livonia, Michigan 48150

APPLICATION FOR FINAL PAYMENT

NOVI PROJECT NO.: 18-8101 FINAL PROJECT: BOSCO PROPERTY PARK **PAYMENT NO.:**

CIP NO.: N/A

ENGINEER: Spalding DeDecker

905 South Boulevard East Rochester, Michigan 48037

(248) 844-5400

DATES OF ESTIMATE

CONTRACTOR:

ORIGINAL: \$1,931,663.68 ORIGINAL: January 14, 2019 FROM: March 3, 2020

REVISED: November 1, 2020

FINAL COMPLETION DATES

ACTUAL: **REVISED:** \$2,029,955.87 November 1, 2020 TO: October 8, 2020

COST OF COMPLETED WORK TO DATE SECTION 1.

Item	BOSCO PROPERTY PARK - DIVISION GL# 400-691.00-977.028	ON 1	(CONTRACT ITEMS (Original)	(CONTRACT ITEMS	(Revised)		THIS PERIOD			TOTAL TO DATE	
No.	Description of Item	Unit	Quantity	Cost/Unit	Total Amt	Quantity	Cost/Unit	Total Amt	Quantity	Amount	%	Quantity	Amount	%
0	Constr. Inspection "Crew Day"	CD	60.00	\$ 700.00	\$ 42,000.00	60.00	\$ 700.00	\$ 42,000.00				97.00	\$ 67,900.00	162%
1	Bonds, Insurance and Mobilization	LS	1.00	\$ 175,000.00	\$ 175,000.00	1.00	\$ 175,000.00	\$ 175,000.00				1.00	\$ 175,000.00	100%
2	Pre-Construction Audio-Visual	LS	1.00	\$ 4,237.75	\$ 4,237.75	0.00	\$ 4,237.75	\$ -				0.00		
3	Soil Erosion Control Measures	LS	1.00	\$ 6,325.00	\$ 6,325.00	1.00	\$ 6,325.00	\$ 6,325.00	0.50	\$ 3,162.50	50%	1.00	\$ 6,325.00	100%
4	Temp Traffic Control Devices	LS	1.00	\$ 14,398.00	\$ 14,398.00	1.00	\$ 14,398.00	\$ 14,398.00				1.00	\$ 14,398.00	100%
5	Tree Protection Fencing	LF	1000.00	\$ 4.60	\$ 4,600.00	0.00	\$ 4.60	\$ -				0.00		
6	Site Grading, Complete	LS	1.00	\$ 299,000.00	\$ 299,000.00	1.00	\$ 299,000.00	\$ 299,000.00				1.00	\$ 299,000.00	100%
7	Irrigation Well	LS	1.00	\$ 9,200.00	\$ 9,200.00	1.00	\$ 9,200.00	\$ 9,200.00				1.00	\$ 9,200.00	100%
8	Subgrade Undercut (As Needed)	CY	1950.00	\$ 17.25	\$ 33,637.50	36.92	\$ 17.25	\$ 636.87				36.92	\$ 636.87	100%
9	Culv, CI F, CSP, 12-inch	LF	76.00	\$ 43.70	\$ 3,321.20	234.00	\$ 43.70	\$ 10,225.80				234.00	\$ 10,225.80	100%
10	Culv, CI F, CSP, 15-inch	LF	94.00	\$ 47.15	\$ 4,432.10	94.00	\$ 47.15	\$ 4,432.10				94.00	\$ 4,432.10	100%
11	Culv, End Section, Metal, 12-inch	EA	6.00	\$ 172.50	\$ 1,035.00	6.00	\$ 172.50	\$ 1,035.00				6.00	\$ 1,035.00	100%
12	Culv, End Section, Metal, 15-inch	EA	2.00	\$ 172.50	\$ 345.00	2.00	\$ 172.50	\$ 345.00				2.00	\$ 345.00	100%
13	Culv End Sect, Conc, 12-inch	EA	10.00	\$ 517.50	\$ 5,175.00	16.00	\$ 517.50	\$ 8,280.00				16.00	\$ 8,280.00	100%
14	Culv End Sect, Conc, 24-inch	EA	2.00	\$ 747.50	\$ 1,495.00	2.00	\$ 747.50	\$ 1,495.00				2.00	\$ 1,495.00	100%
15	Culv End Sect, Conc, 30-inch	EA	1.00	\$ 920.00	\$ 920.00	1.00	\$ 920.00	\$ 920.00				1.00	\$ 920.00	100%
16	Culv End Sect, Conc, 36-inch	EA	2.00	\$ 920.00	\$ 1,840.00	2.00	\$ 920.00	\$ 1,840.00				2.00	\$ 1,840.00	100%
17	Sewer C76, CI IV, 12-inch, Tr A	LF	2268.00	\$ 34.50	\$ 78,246.00	2389.00	\$ 34.50	\$ 82,420.50				2389.00	\$ 82,420.50	100%
18	Sewer C76, Cl IV, 12-inch, Tr B	LF	125.00	\$ 41.40	\$ 5,175.00	0.00	\$ 41.40	\$ -				0.00		
19	Sewer C76, CI IV, 15-inch, Tr A	LF	1031.00	\$ 37.95	\$ 39,126.45	1070.00	\$ 37.95	\$ 40,606.50				1070.00	\$ 40,606.50	100%
20	Sewer C76, Cl IV, 15-inch, Tr B	LF	38.00	\$ 44.85	\$ 1,704.30	38.00	\$ 44.85	\$ 1,704.30				38.00	\$ 1,704.30	100%
21	Sewer C76, Cl IV, 18-inch, Tr A	LF	581.00	\$ 48.30	\$ 28,062.30	585.00	\$ 48.30	\$ 28,255.50				585.00	\$ 28,255.50	100%
22	Sewer C76, Cl IV, 21-inch, Tr A	LF	139.00	\$ 51.75	\$ 7,193.25	173.00	\$ 51.75	\$ 8,952.75				173.00	\$ 8,952.75	100%
23	Sewer C76, Cl IV, 21-inch, Tr B	LF	34.00	\$ 60.95	\$ 2,072.30	0.00	\$ 60.95	\$ -				0.00		
24	Sewer C76, Cl IV, 24-inch, Tr A	LF	531.00	\$ 57.50	\$ 30,532.50	546.00	\$ 57.50	\$ 31,395.00				546.00	\$ 31,395.00	100%



SUBTOTAL

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

100%

1,686,192.04

APPLICATION FOR FINAL PAYMENT

PROJECT: BOSCO PROPERTY PARK NOVI PROJECT NO.: 18-8101 PAYMENT NO.: FINAL

\$ 1,720,351.18

CIP NO.:

N/A

	SECTION 4							COST OF COMPLETED WORK TO DATE									
	SECTION 1.		1				COST OF CONFEETED WORK TO DATE							Ī			
	BOSCO PARK - DIVISION 1, Contin	nued		CONTRACT	ITEMS (Ori	iginal)	(CONTRACT ITEM	S (Re	vised)		THIS PERIOD			7	TOTAL TO DATE	
Item	GL# 400-691.00-977.028	luou				giriai)	·										
No.	Description of Item	Unit	Quantity	Cost/U	nit	Total Amt	Quantity	Cost/Unit		Total Amt	Quantity	Amount	%	Quantity		Amount	%
25	Sewer C76, Cl IV, 24-inch, Tr B	LF	36.00	\$	74.75 \$	2,691.00	0.00	\$ 74.75						0.00			
26	Sewer C76, CI IV, 30-inch, Tr A	LF	154.00	\$	33.25 \$	9,740.50	154.00	\$ 63.25	\$	9,740.50				154.00	\$	9,740.50	100%
27	Sewer C76, CI IV, 36-inch, Tr A	LF	255.00	\$	30.50 \$	20,527.50	247.00	\$ 80.50	\$	19,883.50				247.00	\$	19,883.50	100%
28	Dr Structure, 24-inch Dia.	EA	6.00	\$ 1,72	25.00 \$	10,350.00	6.00	\$ 1,725.00	\$	10,350.00				6.00	\$	10,350.00	100%
29	Dr Structure, 48-inch Dia.	EA	31.00	\$ 4,4	27.50 \$	137,252.50	31.00	\$ 4,427.50	\$	137,252.50				31.00	\$	137,252.50	100%
30	Dr Structure, 48-inch Dia, Over Ex.	EA	1.00	\$ 8,6	25.00 \$	8,625.00	0.00	\$ 8,625.00						0.00			
31	Dr Structure, 60-inch Dia.	EA	2.00	\$ 13,2	25.00 \$	26,450.00	2.00	\$ 13,225.00	\$	26,450.00				2.00	\$	26,450.00	100%
32	Str Rehab Type II: Structure Adjust	EA	1.00	\$ 9	77.50 \$	977.50	0.00	\$ 977.50						0.00			
33	Structure Cover, Type B	EA	1.00	\$ 8	5.00 \$	805.00	1.00	\$ 805.00	\$	805.00				1.00	\$	805.00	100%
34	Outlet Control Structure, 48-inch	EA	2.00	\$ 6,5	55.00 \$	13,110.00	2.00	\$ 6,555.00	\$	13,110.00				2.00	\$	13,110.00	100%
35	Outlet Control Structure, 60-inch	EA	1.00	\$ 7,7	5.00 \$	7,705.00	1.00	\$ 7,705.00	\$	7,705.00				1.00	\$	7,705.00	100%
36	Underdrain, 6-inch, w/ Geo Wrap	LF	17902.00	\$	9.20 \$	164,698.40	17609.00	\$ 9.20	\$	162,002.80				17609.00	\$	162,002.80	100%
37	HMA Surface, Rem, Modified	SY	312.00	\$	17.25 \$	5,382.00	276.31	\$ 17.25	\$	4,766.35				276.31	\$	4,766.35	100%
38	Curb and Gutter, Conc, Remove	LF	406.00	\$	17.25 \$	7,003.50	276.00	\$ 17.25	\$	4,761.00				276.00	\$	4,761.00	100%
39	Agg Base, 6-inch, Limestone	SY	610.00	\$	10.35 \$	6,313.50	1382.50	\$ 10.35	\$	14,308.88				1382.50	\$	14,308.88	100%
40	Geotextile, Separator	SY	2918.00	\$	6.90 \$	20,134.20	2994.00	\$ 6.90	\$	20,658.60				2994.00	\$	20,658.60	100%
41	Aggregate, 4-inch, 22X	SY	3131.00	\$	10.35 \$	32,405.85	2994.00	\$ 10.35	\$	30,987.90				2994.00	\$	30,987.90	100%
42	Aggregate, 8-inch, 22A	SY	17000.00	\$	9.77 \$	166,090.00	16754.36	\$ 9.77	\$	163,690.10				16754.36	\$	163,690.10	100%
43	Aggregate, 8-inch, 21AA	SY	1582.00	\$	11.50 \$	18,193.00	1697.03	\$ 11.50	\$	19,515.85				1697.03	\$	19,515.85	100%
44	Shoulder, Class I, 8-inch	SY	250.00	\$	17.25 \$	4,312.50	0.00	\$ 17.25						0.00			
45	Sidewalk, Conc, 4-inch	SF	5021.00	\$	4.49 \$	22,544.29	5021.00	\$ 4.49	\$	22,544.29				5021.00	\$	22,544.29	100%
46	Sidewalk, Conc, 6-inch	SF	107.00	\$	5.64 \$	603.48	224.00	\$ 5.64	\$	1,263.36				224.00	\$	1,263.36	100%
47	Curb and Gutter, Conc, Modified	LF	384.00	\$	31.57 \$	12,122.88	463.00	\$ 31.57	\$	14,616.91				463.00	\$	14,616.91	100%
48	Conc, Pavt, Nonreinf, 8-inch	SY	19.00	\$	91.72 \$	1,742.68	18.67	\$ 91.72	\$	1,712.41				18.67	\$	1,712.41	100%
49	HMA, 3C	TON	204.00	\$	99.00 \$	20,196.00	224.74	\$ 99.00	\$	22,249.26				224.74	\$	22,249.26	100%
50	HMA, 4C	TON	185.00	\$	99.00 \$	18,315.00	217.64	\$ 99.00	\$	21,546.36				217.64	\$	21,546.36	100%
51	HMA, 5E1	TON	193.00	\$ 1	5.00 \$	20,265.00	254.90	\$ 105.00	\$	26,764.50				254.90	\$	26,764.50	100%
52	Regrade Ditch	LF	405.00	\$	23.00 \$	9,315.00	425.00	\$ 23.00	\$	9,775.00				425.00	\$	9,775.00	100%
53	Perm Pvmt Mrkg, "Accessible"	EA	9.00	\$	33.25 \$	569.25	9.00	\$ 63.25	\$	569.25				9.00	\$	569.25	100%
54	Perm Pvmt Mrkg, Blue, 4-inch	LF	500.00	\$	2.88 \$	1,440.00	529.00	\$ 2.88	\$	1,523.52				529.00	\$	1,523.52	100%
55	Perm Pvmt Mrkg, White, 4-inch	LF	65.00	\$	3.80 \$	897.00	503.76	\$ 13.80	\$	6,951.89				503.76	\$	6,951.89	100%
56	Conc Parking Block, 8-foot Long	EA	48.00	\$ 1	72.50 \$	8,280.00	0.00	\$ 172.50						0.00			
57	Dumpster Enclosure, Complete	EA	1.00	\$ 28,7	50.00 \$	28,750.00	1.00	\$ 28,750.00	\$	28,750.00				1.00	\$	28,750.00	100%
58	Irrigation	LS	1.00	\$ 152,2	50.00 \$	152,250.00	1.00	\$ 152,250.00	\$	152,250.00				1.00	\$	152,250.00	100%
59	Gate, 20-feet	EA	1.00	\$ 3,2	20.00 \$	3,220.00	1.00	\$ 3,220.00	\$	3,220.00				1.00	\$	3,220.00	100%
	TOTAL FROM THIS SHEET				\$	963,277.53			\$	959,724.72		\$ -			\$	959,724.72	
	TOTAL FROM OTHER SHEET				\$	757,073.65			\$	726,467.32		\$ 3,162.50			\$	726,467.32	

\$ 1,686,192.04

3,162.50



SUBTOTAL

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

1,745,756.29 100%

APPLICATION FOR FINAL PAYMENT

PROJECT: BOSCO PROPERTY PARK NOVI PROJECT NO.: 18-8101 PAYMENT NO.: FINAL

\$ 1,880,229.93

CIP NO.: N/A

	SECTION 1.					COST OF COMPLETED WORK TO DATE									
ltem	BOSCO PARK - DIVISION 1, Conti GL# 400-691.00-977.028	nued		CONTRACT ITEMS	(Original)	CONTRACT ITEMS (Revised)			THIS PERIOD			TOTAL TO DATE			
No.	Description of Item	Unit	Quantity	Cost/Unit	Total Amt	Quantity	Cost/Unit	Total Amt	Quantity	Amount	%	Quantity	Amount	%	
60	Gate, 30-feet	EA	3.00	\$ 3,392.50	\$ 10,177.50	3.00	\$ 3,392.50	\$ 10,177.50				3.00	\$ 10,177.50	100%	
61	Bike Rack	EA	1.00	\$ 1,150.00	\$ 1,150.00	1.00	\$ 1,150.00	\$ 1,150.00				1.00	\$ 1,150.00	100%	
62	Security Light, Complete	EA	2.00	\$ 21,275.00	\$ 42,550.00	2.00	\$ 21,275.00	\$ 42,550.00				2.00	\$ 42,550.00	100%	
63	Sign, R1-1, Complete	EA	3.00	\$ 396.75	\$ 1,190.25	4.00	\$ 396.75	\$ 1,587.00				4.00	\$ 1,587.00	100%	
64	Sign, R7-8, R7-8P, Complete	EA	2.00	\$ 419.75	\$ 839.50	2.00	\$ 419.75	\$ 839.50				2.00	\$ 839.50	100%	
65	Sign, R7-8, Complete	EA	7.00	\$ 293.25	\$ 2,052.75	7.00	\$ 293.25	\$ 2,052.75				7.00	\$ 2,052.75	100%	
66	Sign, R8-3, Complete	EA	5.00	\$ 143.75	\$ 718.75	5.00	\$ 143.75	\$ 718.75				5.00	\$ 718.75	100%	
67	Sign, Path Ends, Complete	EA	2.00	\$ 488.75	\$ 977.50	1.00	\$ 488.75	\$ 488.75				1.00	\$ 488.75	100%	
68	Novi Marquee	EA	2.00	\$ 3,823.75	\$ 7,647.50	0.00	\$ 3,823.75	\$ -				0.00	\$ -		
69	Restoration	LS	1.00	\$ 92,575.00	\$ 92,575.00	0.00	\$ 92,575.00	\$ -				0.00	\$ -		
	TOTAL FROM THIS SHEET		•		\$ 159,878.75			\$ 59,564.25	•	\$ -		•	\$ 59,564.25		
	TOTAL FROM OTHER SHEETS				\$ 1,720,351.18			\$ 1,686,192.04		\$ 3,162.50			\$ 1,686,192.04		

\$ 1,745,756.29

3,162.50



SUBTOTAL

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

1,760,131.29 100%

APPLICATION FOR FINAL PAYMENT

PROJECT: BOSCO PROPERTY PARK NOVI PROJECT NO.: 18-8101 PAYMENT NO.: FINAL

CIP NO.: N/A

\$ 1,931,663.68

	SECTION 1.							COS	T OF COMPLETED) WORK TO	O DATE					
Item	BOSCO PARK - DIVISION 2 - (TREE GL# 209-691.00-977.028					(Original) CONTRACT ITEMS (Revised)			THIS PERIOD			TOTAL TO DATE				
No.	Description of Item	Unit	Quantity	Cost/Ur	nit	Total Amt	Quantity	Cost/Unit	Total Amt	Quantity	Amount	%	Quantity		Amount	%
70	Tree Plantings, Austrian Pine	EA	61.00	\$ 40	2.50	\$ 24,552.50	0.00	\$ 402.50	\$ -				0.00	\$	-	
71	Tree Plantings, Red Pointe Maple	EA	38.00	\$ 57	5.00	\$ 21,850.00	25.00	\$ 575.00	\$ 14,375.00				25.00	\$	14,375.00	100%
72	Wetland Edge Seed Mix, w/Blanket	SY	175.00	\$ 2	8.75	\$ 5,031.25	0.00	\$ 28.75	\$ -				0.00	\$	-	
				<u> </u>												
				ļ												
				ļ												
				ļ												
				ļ												
				<u> </u>												
				<u> </u>												
<u> </u>		-		-				-					 	-		
				-									<u> </u>			
			-	-												
				-	\dashv								<u> </u>			
	<u> </u>	<u> </u>									<u> </u>		<u> </u>	<u> </u>		
	TOTAL FROM THIS SHEET \$						\$ 14,375.00		\$ -			\$	14,375.00			
	TOTAL FROM OTHER SHEETS				;	\$ 1,880,229.93			\$ 1,745,756.29		\$ 3,162.50			\$	1,745,756.29	

\$ 1,760,131.29

3,162.50

NOVI cityofnovi.org

TOTAL FROM OTHER SHEETS

GRAND TOTAL

CITY OF NOVI

26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

3,162.50

12,270.00

1,760,131.29

\$ 2,029,955.87

1,760,131.29

2,029,955.87 100%

APPLICATION FOR FINAL PAYMENT

PROJECT: BOSCO PROPERTY PARK NOVI PROJECT NO.: 18-8101 PAYMENT NO.: FINAL

CIP NO.: N/A

\$ 1,931,663.68

\$ 1,931,663.68

NEW CONTRACT ITEMS

	SECTION 1.				COST OF COMPLETED WORK TO DATE											
Item						NEW CONTRACT ITEMS				THIS PE	ERIOD			TOTAL TO DATE		
No.	Description of Item	Unit	Division	GL#	Quantity	Cost/Unit	Total Am	:	Quantity	Amo	ount	%	Quantity		Amount	%
73	Tree Plantings, Black Hills Spruce	EA	2	GL# 209-691.00-977.028	25.00	\$ 340.00	\$ 8,5	00.00					25.00	\$	8,500.00	100%
74	Tree Plantings, Skyline Honey Locust	EA	2	GL# 209-691.00-977.028	25.00	\$ 565.00	\$ 14,1	25.00					25.00	\$	14,125.00	100%
75	Tree Plantings, White Pine	EA	2	GL# 209-691.00-977.028	24.00	\$ 340.00	\$ 8,1	60.00					24.00	\$	8,160.00	100%
76	Structure Cover, (EJ1040 Type N cover	EA	1	GL# 400-691.00-977.028	35.00	\$ 650.00	\$ 22,7	50.00					35.00	\$	22,750.00	100%
77	Structure Cover, (EJ1030 Type 01 cover	EA	1	GL# 400-691.00-977.028	3.00	\$ 650.00	\$ 1,9	50.00					3.00	\$	1,950.00	100%
78	Restoration	EA	2	GL# 209-691.00-977.028	1.00	\$ 91,075.00	\$ 91,0	75.00	0.10	\$ 9	9,107.50	10%	1.00	\$	91,075.00	100%
79	Dr Structure, 48-inch Dia.	EA	3	GL# 204-204.00-974.451	0.00	\$ 4,427.50	\$	-					0.00	\$	-	
80	Sewer C76, Cl IV, 12-inch, Tr A	LF	3	GL# 204-204.00-974.451	0.00	\$ 34.50	\$	-					0.00	\$	-	
81	Agg Base, 6-inch, Limestone	SY	3	GL# 204-204.00-974.451	821.00	\$ 10.35	\$ 8,4	97.35					821.00	\$	8,497.35	100%
82	Sidewalk, Conc, 4-inch	SF	3	GL# 204-204.00-974.451	6155.00	\$ 4.49	\$ 27,6	35.95					6155.00	\$	27,635.95	100%
83	Sidewalk, Conc, 6-inch	SF	3	GL# 204-204.00-974.451	410.00	\$ 5.64	\$ 2,3	12.40					410.00	\$	2,312.40	100%
84	Structure Cover, (EJ1040 Type N cover	EA	3	GL# 204-204.00-974.451	0.00	\$ 650.00	\$	-					0.00	\$	-	
85	ADA Detectable Warning Plate	SF	3	GL# 204-204.00-974.451	48.00	\$ 21.56	\$ 1,0	34.88					48.00	\$	1,034.88	100%
86	Relocate Pedestrian Push Button, Comp	EA	3	GL# 204-204.00-974.451	2.00	\$ 5,250.00	\$ 10,5	00.00					2.00	\$	10,500.00	100%
87	Relocate Guy Wire	EA	3	GL# 204-204.00-974.451	1.00	\$ 6,700.00	\$ 6,7	00.00					1.00	\$	6,700.00	100%
88	Topsoil	CY	1	GL# 400-691.00-977.028	4756.00	\$ 14.00	\$ 66,5	34.00					4756.00	\$	66,584.00	100%
89			0	0	0.00	\$ -	\$	-					0.00	\$	-	
90			0	0	0.00	\$ -	\$	-					0.00	\$	-	
91			0	0	0.00	\$ -	\$	-					0.00	\$	-	
92			0	0	0.00	\$ -	\$	-					0.00	\$	-	
93			0	0	0.00	\$ -	\$	-					0.00	\$	-	
94			0	0	0.00	\$ -	\$	-					0.00	\$	-	
95			0	0	0.00	\$ -	\$	-					0.00	\$	-	
96			0	0	0.00	\$ -	\$	-					0.00	\$	-	
97			0	0	0.00	\$ -	\$	-					0.00	\$	-	
98			0	0	0.00	\$ -	\$	-					0.00	\$	-	
99			0	0	0.00	\$ -	\$	-					0.00	\$	-	
100			0	0	0.00	\$ -	\$	-					0.00	\$	-	
	TOTAL FROM THIS SHEET						\$ 269,8	24.58		\$	9,107.50			\$	269,824.58	



BALANCE DUE THIS PAYMENT:

CITY OF NOVI

\$

113,767.80

PURCHASE ORDER NO.

26300 Lee BeGole Dr.
Novi, Michigan 48375
Tel: (248) 347-0454

95681 Tel: (248) 347-0454
Fax: (248) 735-5659

Section 2.							
		APPLICAT	TION FOR FIN	AL PAYMENT			
PROJECT: BOSCO PROPERTY PARK	NOVI PROJI CIP NO.:	ECT NO.:	18-8101 N/A		PAYME	ENT NO.:	FIN
Original Contract Amount:	\$	1,931,663.68		CHANGE (ORDERS		
Change Orders:	\$	98,292.19	<u>No.</u> 1	<u>Date</u> March 25, 2019	\$	Amount 32,722.18	ł
Adjusted Contract Amount to Date:	\$	2,029,955.87	•	April 1, 2019 June 24, 2019	\$ \$	(7,773.75 65,587.62	5)
Total Cost of Work Performed to Date:	\$	2,029,955.87	•	August 9, 2019 February 25, 2020	\$	49,280.00 (41,523.86)
MINUS Retainage: MINUS Inspection "Crew Days": To Date	0% \$ 97.00 \$	- 25,900.00					
This Pay Net Amt. Earned of Contract and Extra Work to Date:	0.00 \$	2,004,055.87	8 9 10				
MINUS L.D.'s: # of days over = \$900	\$	-	10				
Subtotal:	\$	2,004,055.87					_
ADD Incentive "Crew Days", if under:	\$	-		тот	AL: \$	98,292.19)
Subtotal:	\$	2,004,055.87					
MINUS Amount of Previous Payments: 1 \$ 372,788.28	\$	1,890,288.07					
2 \$ 277,775.37 3 \$ 132,802.92				Inspection "Crew Days" A			
4 \$ 423,810.17 5 \$ 214,658.16				Additional "Crew Days" per Total Inspection "Crew Days"		s: 0.00 60.00	4
6 \$ 222,266.32				Inspection "Crew Days" U	•	97.00	┨
7 \$ 136,541.54				Inspection "Crew Days" R		-37.00	
8 \$ 109,645.32				,		•	
9 \$ (0.00)							
10 \$ -			_				



26300 Lee BeGole Dr. Novi, Michigan 48375 Tel: (248) 347-0454 Fax: (248) 735-5659

Section 3.

APPLICATION FOR FINAL PAYMENT NOVI PROJECT NO.: PROJECT: **BOSCO PROPERTY PARK** 18-8101 **PAYMENT NO.: FINAL** CIP NO.: N/A Payment of the above AMOUNT DUE THIS APPLICATION

The undersigned CONTRACTOR certifies that: (1) Any previous progress payments received from OWNER on amount of Work done under the Contract referred to above have been applied to discharge is recommended. in full all obligations of CONTRACTOR incurred in connection with Work covered by prior Applications **CITY OF NOVI** for Payment; (2) title to all Work, materials, and equipment incorporated in said Work of otherwise listed in or covered by this Application for Payment will pass to OWNER at time of payment free and clear of all leins, claims, security interest, and encumberences (except such as are covered by Bond acceptable to OWNER indemnifying OWNER against any such lein, claim security interest, or encumberence); and (3) all Work covered by this Application for Payment is in accordance with the Contract Documents and not defective as that term is defined in the Contract Documents. Aaron J. Staup, Construction Engineer Anglin Civil, LLC **CONTRACTOR - Electronic Signature Certification** Spalding DeDecker CONSULTANT - Electronic Signature Certification

Electronic Signature Certification

All Full Unconditional Waivers of lien have been received from each subcontractor and/or supplier, reviewed and approved by the Consultant. Also, attached to this Final Payment is a copy of the Contractor's Sworn Statement, Consent of Surety, and a new Maintenance and Guarantee Bond (if the amount is greater than the final contract price) or a Maintenance Bond Rider covering the difference between the final contract price and the awarded amount.

CONSENT OF SURETY TO FINAL PAYMENT AIA Document G707		OWNER ARCHITECT CONTRACTOR SURETY
(Instructions on reverse side)	Bond No. RCB0017621	OTHER
TO OWNER: (Name and address) City of Novi 26300 Lee BeGole Drive Novi, MI 48375	ARCHITECT'S F	
PROJECT: (Name and address) Bosco Fields	CONTRACT DA	TED: 10/12/2018
In accordance with the provisions of the Consert name and address of Surety) RLI Insurance Company 9025 N. Lindergh Drive Peoria, II 61615	Contract between the Owner and the Contracto	
on bond of (Insert name and address of Contractor) Anglin Civil, LLC 13000 Newburgh Road Livonia, MI 48150		, SURETY,
hereby approves of the final payment to tany of its obligations to (Insert name and address of Owner) City of Novi 26300 Lee BeGole Drive Novi, MI 48375	he Contractor, and agrees that final payment to	the Contractor shall not relieve the Surety of
as set forth in said Surety's bond.		, OWNER,
IN WITNESS WHEREOF, the Surety has he (Insert in writing the month followed by the numeric	j ,	020
Attest: Gulle O	RLI Insurance (Suretf) Autorize Tammy R. Pitt (Printed name and title	tman, Attorney-in-Fact

POWER OF ATTORNEY

RLI Insurance Company Contractors Bonding and Insurance Company

9025 N. Lindbergh Dr. Peoria, IL 61615 Phone: 800-645-2402

Know All Men by These Presents:

That this Power of Attorney is not valid or in effect unless attached to the bond which it authorizes executed, but may be detached by the approving officer if desired.

Angelo G. Zervos, Gus E. Zervos, Donald W. Burden, Michael Zervos, St	ephen M. Zervos. Tammy R. Pittman, jointly or severally
- Migute 6. 261 vos, Gus B. 261 vos, Bollaid W. Buldell, Milelladi 261 vos, St	Sphen 141. 251403, Tellining R. Fiteman, John of Severally
	1.
in the City of Southfield, State of Michigan full power and authority hereby conferred, to sign, execute, acknowledge bonds and undertakings in an amount not to exceed (\$25,000,000.00) for any single obligation.	
The acknowledgment and execution of such bond by the said Attorney in executed and acknowledged by the regularly elected officers of the Compa	
RLI Insurance Company and/or Contractors Bonding and Insurant following is a true and exact copy of a Resolution adopted by the Board of	
"All bonds, policies, undertakings, Powers of Attorney or other obligat the Company by the President, Secretary, any Assistant Secretary, Treas of Directors may authorize. The President, any Vice President, Se Attorneys in Fact or Agents who shall have authority to issue bonds, po seal is not necessary for the validity of any bonds, policies, undertaking signature of any such officer and the corporate seal may be printed by fa IN WITNESS WHEREOF, the RLI Insurance Company and/or Concaused these presents to be executed by its respective Vice Pres	surer, or any Vice President, or by such other officers as the Board cretary, any Assistant Secretary, or the Treasurer may appoint licies or undertakings in the name of the Company. The corporate s, Powers of Attorney or other obligations of the corporation. The acsimile." attractors Bonding and Insurance Company, as applicable, have
May , 2020 - CORPORATE SEAL SEAL	RLI Insurance Company Contractors Bonding and Insurance Company By: Barton W. Davis Vice President
State of Illinois County of Peoria SS	CERTIFICATE
On this 14th day of May, 2020, before me, a Notary Public, personally appeared Barton W. Davis, who being by me duly sworn, acknowledged that he signed the above Power of Attorney as the aforesaid officer of the RLI Insurance Company and/or Contractors Bonding and Insurance Company and acknowledged said instrument to be the voluntary act and deed of said corporation. By: Catherine D. Glover Notary Public	I, the undersigned officer of RLI Insurance Company and/or Contractors Bonding and Insurance Company, do hereby certify that the attached Power of Attorney is in full force and effect and is irrevocable; and furthermore, that the Resolution of the Company as set forth in the Power of Attorney, is now in force. In testimony whereof, I have hereunto set my hand and the seal of the RLI Insurance Company and/or Contractors Bonding and Insurance Company this day of RLI Insurance Company Contractors Bonding and Insurance Company
CATHERINE D. GLOVER OFFICIAL SEAL PUBLIC FORM NOTARY Public - State of Illinois BY Commission Expires March 24, 2024	By: Jeffrey D. Fick. Corporate Secretary



P.O. Box 3967 Peoria, IL 61612-3967 Phone: 309-692-1000 Fax: 309-683-1610

RIDER

TO BE ATTACHED TO AND FORM PAR	T OF BOND/POLICY NO	RCB0017621	
It is hereby m	nutually agreed and understoo Anglin Civil	od by the Principal,	
and RLI Insurance Company Maintenance and Guarantee Bond da		ity of Novi as Obligee, for the	
	(Identify item(s) to be change	ed)	
	/policy has/have been change creased FROM: \$1,931,663.		
Nothing contained herein shall vary, alte except as set forth above. This Rider becomes effective on Standard Time.	•		, .
Signed this <u>28th</u> day of <u>Ju</u>	l <u>y</u> , <u>2020</u> .		
		Company and/or nding and Insurance Compa	i ny
	Tammy R. Pitti	man	Attorney in Fact

Attorney in Fact

POWER OF ATTORNEY

RLI Insurance Company Contractors Bonding and Insurance Company

9025 N. Lindbergh Dr. Peoria, IL 61615 Phone: 800-645-2402

Know All Men by These Presents:

That this Power of Attorney is not valid or in effect unless attached to the bond which it authorizes executed, but may be detached by the approving officer if desired.

together, the "Company") do hereby make, constitute and appoint: <u>Angelo G. Zervos, Gus E. Zervos, Donald W. Burden, Michael Zervos, Ste</u>	onhan M. Zarwag. Tammy P. Dittman, jointly or acyonally
Angelo G. Zervos, Gus E. Zervos, Bollalu W. Burdell, Michael Zervos, Ste	phen ivi. Zervos, Tahiniy R. Fitunan, Johnty of Severany
in the City of Southfield, State of Michigan full power and authority hereby conferred, to sign, execute, acknowledge bonds and undertakings in an amount not to exceed (\$25,000,000.00) for any single obligation.	
The acknowledgment and execution of such bond by the said Attorney in lexecuted and acknowledged by the regularly elected officers of the Compa	Fact shall be as binding upon the Company as if such bond had been ny.
RLI Insurance Company and/or Contractors Bonding and Insuran following is a true and exact copy of a Resolution adopted by the Board of	
"All bonds, policies, undertakings, Powers of Attorney or other obligation the Company by the President, Secretary, any Assistant Secretary, Treas of Directors may authorize. The President, any Vice President, Sec Attorneys in Fact or Agents who shall have authority to issue bonds, policies are is not necessary for the validity of any bonds, policies, undertakings signature of any such officer and the corporate seal may be printed by factorized.	urer, or any Vice President, or by such other officers as the Board retary, any Assistant Secretary, or the Treasurer may appoint icies or undertakings in the name of the Company. The corporate, Powers of Attorney or other obligations of the corporation. The
IN WITNESS WHEREOF, the RLI Insurance Company and/or Cont caused these presents to be executed by its respective Vice Presi May, 2020	dent with its corporate seal affixed this 14th day of
ORPORA CORPORA CORPORA SEAL	RLI Insurance Company Contractors Bonding and Insurance Company By: Barton W. Davis Vice President
State of Illinois SS	
County of Peoria S	CERTIFICATE
On this 14th day of May, 2020, before me, a Notary Public, personally appeared Barton W. Davis, who being by me duly sworn, acknowledged that he signed the above Power of Attorney as the aforesaid officer of the RLI Insurance Company and/or Contractors Bonding and Insurance Company and acknowledged said instrument to be the voluntary act and deed of said corporation. By: Catherine D. Glover Notary Public	I, the undersigned officer of RLI Insurance Company and/or Contractors Bonding and Insurance Company, do hereby certify that the attached Power of Attorney is in full force and effect and is irrevocable; and furthermore, that the Resolution of the Company as set forth in the Power of Attorney, is now in force. In testimony whereof, I have hereunto set my hand and the seal of the RLI Insurance Company and/or Contractors Bonding and Insurance Company this day of RLI Insurance Company Contractors Bonding and Insurance Company Contractors Bonding and Insurance Company
CATHERINE D. GLOVER OFFICIAL SEAL PRINTED NOTATIVE PUBLIC PRINTED OF UNITED OF MATCH 24, 2024	By: Jeffrey D. Fick Corporate Secretary

SWORN STATEMENT

STATE OF MICHIGAN, COUNTY								
<u>CIVIL</u> OAKLAND	(com County, M		ne contractor for	an improveme	ent to the followin	g described real	property situate	ea in
	·	_	Anniinatian Na.	FINIAL				
Project Title: _BOSCO FIELDS Location (city & state):N						9/15/2020		
Project No(s):N						0/13/2020		_
			CONTRACT NO					
Purchase Order No:								
That the following is a statemen	at of anch contracto	rand cumplion fa	ur vuhiah mavenan	+ ic dua hu+ un	n a i d i t b i b a ma t	ha Cantrastar ha	s contracted for	r narfarmanaa
That the following is a statemer relative to the Construction agr					•			•
		[A]	[B]	[C]	[D]	[B+C+D=E]	[F]	[A - E - F = G]
							TOTAL	
0.10.00.1TD 4.0TO D	TYPE OF	TOTAL	AMOUNT	AMOUNT	AMOUNT	AMOUNT	CUMULATIVE	BALANCE
SUBCONTRACTOR, SUPPLIER OR LABORER	IMPROVEMENT FURNISHED	CONTRACT PRICE	ALREADY PAID	INVOICED	CURRENTLY OWING	BILLED TO DATE	RETENTION WITHHELD	TO COMPLETE
SUPPLIER OR LABORER	FUNNISHED	PRICE	PAID	(NOT PAID)	OWING	TO DATE	WITHHELD	COMPLETE
GM & Sons	Concrete	66,924.40	66,924.40	-	-	66,924.40		-
Future Fence	Gates	19,419.99	19,419.99	-	-	19,419.99	-	-
Rauhorn Electrc	Crosswalk Elec	14,656.00	14,656.00		-	14,656.00		-
Cribley Well Drilling	Well	25,826.80	25,826.80			25,826.80		-
Halligan Electric	Elec	33,305.25	33,305.25			33,305.25		-
Maj's Services	Silt Fence	5,750.00	5,750.00			5,750.00		-
						-		-
						-		-
						-		-
						-		-
						-		-
						-		-
GRAND TOTA	ALS	165,882.44	165,882.44	-	-	165,882.44	-	-
Under penalty of perjury, the D	eponent states the o	contractor has no	ot procured mate	erial from, or s	ubcontracted with	, any person oth	er than those se	t forth above and
owes no money for the Improve	ement other than th	e sums set forth	above.					
(Signature)								
(Name & Title)Nic Faust, Pr								
(Company Name) ANGLIN C								
12. Family Tames	····=		_					



My/our contract with	Anglin Civil	to provide
	(Prime Contracting Party)	
concrete construction (Type of service	for the improv	vement of the property
described asBosco	Fields (Project Name)	
	satisfied, by signing this waiver, a certy are hereby waived and release	
owner or lessee of the prop Notice of Furnishing from n the owner, lessee, or design us, the owner, lessee, or des	rided to property that is a resident perty or the owner's or lessee's dependence or us or if I/we are not required has not received this waiver designed may not rely upon it without phone, or personally, to verify that	esignee has received a fired to provide one, and irectly from me/one of at contacting me/one of it is authentia.
	Karl Schweitzer (Printed Name of L	ien Claimant)
	General Manager (Title of Lien	Claimant)
Company Name.	& Sons, Inc. Lake Road, Whitmore Lake, MI 48	
724 020 124		
Telephone:		



My/our contract with

FULL UNCONDITIONAL WAIVER OF LIEN

Anglin Civil Constructors

with contract with		to provide
	(Prime Contracting Party)	
4	een Wall and Gates for the e of service)	improvement of the property
described as	Bosco Fields	
	(Project Name)	
having been fully pa lien rights against such	id and satisfied, by signing this watch property are hereby waived and r	aiver, all my/our construction released.
Notice of Furnishing the owner, lessee, or us, the owner, lessee	he property or the owner's or less from me/one or us or if I/we are no designee has not received this was, or designee may not rely upon it by telephone, or personally, to verif	see's designee has received a of required to provide one, and niver directly from me/one of without contacting me/one of
Signed on:9/30/20		are of Lien Claimant)
	Larry L. Berry	are of Element)
	(Printed N	lame of Lien Claimant)
	Contract Adminis	trator
	(Title	e of Lien Claimant)
Company Name:	Future Fence Company	
Address:	23450 Regency Park Drive War	rren, MI 48089
Telephone: 586/7	55-0900	

to provide



My/our contract with

FULL UNCONDITIONAL WAIVER OF LIEN

Anglin Civil L.L.C.

	(Prime Contracting Party)
electrical work	for the improvement of the property
(Type of service)	
described as Bosco Fields	
	(Project Name)
having been fully paid and satisfied, lien rights against such property are he	by signing this waiver, all my/our construction ereby waived and released.
owner or lessee of the property or the Notice of Furnishing from me/one or us the owner, lessee, or designee has no us, the owner, lessee, or designee may us, either in writing, by telephone, or p	operty that is a residential structure and if the ne owner's or lessee's designee has received as or if I/we are not required to provide one, and it received this waiver directly from me/one of y not rely upon it without contacting me/one of personally, to verify that it is authentic.
Signed on:08/21/20	(Signature of Lien Claimant)
	(- 8
	Laura Ferraro
-	(Printed Name of Lien Claimant)
	Controller
_	(Title of Lien Claimant)
Company Name: Rauhorn Elect	
Address: 14140 33 Mile Road	, Bruce Twp, MI 48065
Telephone: 586-992-0400	



	My/our contract with Anglin Civil, LLC to provide (Prime Contracting Party)
	Well Hook Up for the improvement of the property
	described as Bosco Fields (Project Name)
	having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.
	If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic.
	Signed on: 8/17/2020 Signature of View Claimant)
rible	y Drilling Co., Inc. (Printed Name of Lien Claimant)
ampi 830 0 D	TER, MI 48130-9786 TER Treatment (Title of Lien Claimant)
	Company Name:
	Address:
	Telephone:



My/our contract with
described as BOSCO SOCUE FILLS (Project Name)
having been fully paid and satisfied, by signing this waiver, all my/our construction lien rights against such property are hereby waived and released.
If the improvement is provided to property that is a residential structure and if the owner or lessee of the property or the owner's or lessee's designee has received a Notice of Furnishing from me/one or us or if I/we are not required to provide one, and the owner, lessee, or designee has not received this waiver directly from me/one of us, the owner, lessee, or designee may not rely upon it without contacting me/one of us, either in writing, by telephone, or personally, to verify that it is authentic. Signed on: 9999000
Printed James Lien Claimant)
CON-180 / Isle (Title of Lien Claimant)
Company Name: Halligan Electric Inc. Address: 705 Kelso St. Flint, MI 48506
Telephone: $90-238-8581$



My/our contract with Anglin Civil	to provide
•	(Prime Contracting Party)
Erosion Control - Silt fence (Type of service)	for the improvement of the property
described as Bosco Fields	(Project Name)
having been fully paid and satisfied lien rights against such property are l	, by signing this waiver, all my/our construction hereby waived and released.
owner or lessee of the property or Notice of Furnishing from me/one or the owner, lessee, or designee has r us, the owner, lessee, or designee m	property that is a residential structure and if the the owner's or lessee's designee has received a rus or if I/we are not required to provide one, and not received this waiver directly from me/one of ay not rely upon it without contacting me/one of a personally, to verify that it is authentic.
Signed on:	Lori Guinard (Signature of Lien Claimant)
	Lori Guinard (Printed Name of Lien Claimant)
Company Name: Maj's Services I	nc.
Address: 9864 E Grand River Ste	110-179, Brighton, MI 48116
Telephone: <u>517-521-1340</u>	
